#### **Foreward**

ASBESTOS SURVEY REPORT FOR JOPLING HOUSE, JOHN STREET, SUNDERLAND, SR1 1DP.

I have enclosed for your information and retention the most recent asbestos survey (Management) which applies to the property stated above. The purpose of the survey is to identify as far as possible, the materials containing asbestos fibres in your property.

The attached report is divided in sections so as to give as much information as possible, a basic reference section for use by premises managers and a more detailed report for use by contractors on site etc.

#### Plan of the Building and Sample Locations

This contains a plan of the building and identifies where asbestos samples have been taken from.

#### **Photographs of Areas Sampled**

This section contains photographs of all the areas where samples were taken. These photographs can be used when carrying out the periodic inspections to see if there has been any change or deterioration in its condition.

#### Survey Information

This section contains the survey information as printed from the central database held at Land and Property. It describes the type of asbestos present, its location, condition etc. Contractors should be shown this section along with the others when they are shown the register prior to starting any work.

#### **Priority Risk Assessments**

This section contains assessments which have been created using information from the survey and information on your property. This assessment helps to determine how often periodic checks on any asbestos need to be carried out by your Samo.

#### **5 Simple Steps to Asbestos Management**

This section details procedures for managing asbestos in your property. It gives guidance on the register, the inspections, any planned work and what to do when contractors arrive on site.

#### **Commonly asked Questions**

This section covers questions most commonly asked and can be referred to as/when the need arises.

The building has been surveyed as comprehensively as possible, all potentially fibrous materials have been examined and where necessary analysed by competent UKAS accredited analysts and the findings of both recorded in the report.

This report is an important document and must be referred to before any building works are carried out. The report must be kept with your handbook and the checklists completed on a regular basis. You will be reminded when your specific checklists are due for submission.

## <u>Information for Employees Working in Premises where Asbestos</u> Containing Materials Exist.

Asbestos is made up of fibrous materials, which are flexible, mechanically strong and resistant to stretching, heat and chemicals. As a consequence asbestos has been used extensively in buildings. Examples of asbestos containing materials found in buildings include exterior asbestos cement cladding; gutters and pipes; fireproof sprays on structural steel joists; insulation boards in service ducts and wall partitions; ceiling and floor tiles and pipe and boiler lagging.

Asbestos containing products can produce very small fibrous dust particles, which can not be seen by the naked eye. It is only when these fibres become airborne, due to damage, deterioration, disturbance etc, that there is a risk to health.

# If asbestos is maintained in good condition and is not disturbed or damaged it does not pose a health risk.

The authority has a management system for ensuring that you are not exposed to asbestos containing materials that are in poor condition and may pose a health risk. This system is based on sound principals laid down by legislation and associated codes of practice and guidance.

It is not appropriate simply to remove all asbestos containing materials in buildings. Asbestos materials that are sound, undamaged and not releasing dust should be left alone. Any disturbance to such materials, however carefully controlled, will release fibres and be counter-productive.

Within the building you occupy, your department has nominated a Site Asbestos Monitoring Officer (SAMO). This individual is responsible for inspecting the asbestos containing materials to ensure they are not in a dangerous condition. Should you have any concerns about suspect materials within your premises you should contact the SAMO.

#### Restrictions on use, distribution and publication of the report

We accept no responsibility or liability for the consequences of this document being used for purpose other than for which it was commissioned.

To the extent that the document is based on the information available at the time of writing, Sunderland City Council accepts no liability for any consequences should this report be used for any other purpose

If you require any further information regarding the report or its application please contact Caroline Bage, Asbestos Manager on Tel: 07557 938966.

Yours sincerely,

Neil Guthrie Director of Development and Property



# Sunderland City Council

Control of Asbestos Regulations 2012

#### **Asbestos Register for**

Jopling House, John Street, Sunderland



UPRN: - J171340 TF Ref:

Location of register:-

Premises Manager / Samo: - Tenant Date: 13 February 2025

**Contact Numbers List: -**

Caroline Bage Asbestos Manager – 07557 938966

#### **Contents**

		Section
•	Plan of building and sample locations	1
•	Photographs of areas sampled	2
•	Survey information	3
•	Asbestos Management Plan, Priority Assessments,	4
•	Contacts Form, Code of Practice	4
•	5 Simple Steps of Asbestos Management	5
•	Commonly asked questions	6
Aр	<u>pendices</u>	
•	Form 1 – Visitor Register	7
•	Form 2 – Periodic Return Checklist and Schedule	8
•	Form 3 – Works Notification Form	9
•	Form 4 – Registration of All Disturbances	10
•	Form 5 –Training Records	11

## Plan of Building and Samples Location

Item No.	Sample Ref.	Area Sampled	Location Name	Inspection Frequency
1.	NO000251	Floor tiles Grey/pink	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk
2.	NO000252	Debris/Residue to ceiling void and floor	Z-Sub level 1 Shop Floor (Room Z1/001)	Removed Sept 2023
3.	NO000253	Pipework Gaskets	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk
4.	Presumed	Pipework Gaskets to deeply recessed to sample	Z-Sub level 1 Shop Floor (Room Z1/001)	This item is classed as very low risk and should be inspected every 12 months
5.	NO000254	Cable braiding insulation	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk
6.	NO000255	Cable braiding insulation	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk
7.	NO000256	Fuses flashguards	Z-Sub level 1 Shop Floor (Room Z1/001)	This item is classed as very low risk and should be inspected every 12 months
8.	NO000257	Debris/Residue	Z-Sub level 1 Shop Floor (Room Z1/001)	Removed Sept 2023
9.	NO000258	Debris/Residue from boiler room entrance across to	Z-Sub level 1 Shop Floor (Room Z1/001)	Removed Sept 2023
		stairs and adjacent areas		
10.	NO000259	Debris/Residue to redundant pump	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk
11.	NO000264	Debris/Residue to floor adjacent stairwell	Z-Sub level 1 Shop Floor (Room Z1/001)	Removed Sept 2023
12.	NO000266	Ceiling tile behind metal grid tiles	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk
13.	NO000267	Ductwork joints	Z-Sub level 1 Shop Floor (Room Z1/001)	This item is classed as low risk and should be inspected every 6 months
14.	NO000260	Floor tile on shelving	Z-Sub level 1 Store Room (Room Z1/006)	No Risk
15.	NO000261	Debris/Residue to redundant pipe hanger	Z-Sub level 1 Switch Room (Room Z1/007)	Removed Sept 2023
16.	As NO000254	Cable braiding insulation	Z-Sub level 1 Switch Room (Room Z1/007)	No Risk
17.	NO000256	Fuses flashguards	Z-Sub level 1 Switch Room (Room Z1/007)	This item is classed as very low risk and should be inspected every 12 months
18.	NO000302	Door seal/gasket discarded on floor	Z-Sub level 1 Switch Room (Room Z1/007)	No Risk
19.	NO000262	Debris/residue to	Z-Sub level 1 Plant	Removed Sept 2023

		floor	Room (Room Z1/008)	
20.	NO000263	Ductwork joints	Z-Sub level 1 Plant Room (Room Z1/008)	This item should be removed by a licensed contractor asap
21.	As NO000263	Ductwork joints	Z-Sub level 1 Staircase/Stairwell (Room Z1/009)	This item is classed as low risk and should be inspected every 6 months
22.	NO000265	Wall	Z-Sub level 1 Staircase/Stairwell (Room Z1/009)	This item should be removed by a licensed contractor asap
23.	As NO000265	Debris/Residue foot of stairwell and adjacent areas	Z-Sub level 1 Staircase/Stairwell (Room Z1/009)	Removed Sept 2023
24.	NO000301	Cable braiding insulation remnants to wall	Z-Sub level 1 Staircase/Stairwell (Room Z1/009)	No Risk
25.	NO000268	Floor tile	Z-Sub level 1 Store Room (Room Z1/010)	No Risk
26.	NO000269	Floor jointing compound	Z-Sub level 1 Store Room (Room Z1/014)	No Risk
27.	As NO000269	Floor jointing compound	Z-Sub level 1 Store Room (Room Z1/017)	No Risk
28.	NO000270	Floor tile red	Z-Sub level 1 Store Room (Room Z1/017)	No Risk
29.	As NO000269	Floor jointing compound	Z-Sub level 1 Tank Room (Room Z1/018)	No Risk
30.	NO000272	Floor tile cream	Z-Sub level 1 Tank Room (Room Z1/018)	No Risk
31.	As NO000256	Fuses flashguards	Z-Sub level 1 Tank Room (Room Z1/018)	This item is classed as very low risk and should be inspected every 12 months
32.	NO000271	Pipework gaskets	Z-Sub level 1 Tank Room (Room Z1/018)	This item is classed as very low risk and should be inspected every 12 months
33.	As NO000271	Pipework gaskets	Z-Sub level 1 Tank Room (Room Z1/018)	This item is classed as low risk and should be inspected every 6 months
34.	NO000273	Debris/Residue	Z-Sub level 1 Tank Room (Room Z1/018)	Removed Sept 2023
35.	NO000274	Floor tile pink grey	Z-Sub level 1 Shop Floor (Room Z1/019)	No Risk
36.	Presumed	Pipework Gaskets to deeply recessed to sample	Z-Sub level 1 Shop Floor (Room Z1/019)	This item is classed as very low risk and should be inspected every 12 months
37.	As NO000257	Debris/Residue	Z-Sub level 1 Shop Floor (Room Z1/019)	Removed Sept 2023
38.	As NO000266	Ceiling tile behind metal grid tiles	Z-Sub level 1 Shop Floor (Room Z1/019)	No Risk
39.	As NO000272	Floor tile cream	Z-Sub level 1 Shop Floor (Room Z1/019)	No Risk
40.	As	Ductwork joints	Z-Sub level 1 Shop	This item is classed as

	NO000267		Floor (Doors 74/040)	low risk and should be
	NO000267		Floor (Room Z1/019)	inspected every 6
				months
41.	As	Floor tile pink/grey	Z-Sub level 1	No Risk
	NO000251		Staircase/Stairwell	
42.	As	Debris/Reside to	(Room Z1/020)  Z-Sub level 1 Store	Pomovod Sont 2022
42.	NO000273	ceiling void and	Room (Room Z1/021)	Removed Sept 2023
	740000270	floor below	1100m (1100m 2 1702 17	
43.	Presumed	Pipework Gaskets	Z-Sub level 1 Store	This item is classed as
			Room (Room Z1/021)	very low risk and should
				be inspected every 12
44.	As	Cable	Z-Sub level 1 Store	months No Risk
44.	NO000254	braiding/insulation	Room (Room Z1/022)	INO KISK
45.	As	Fuses flashguards	Z-Sub level 1 Store	This item is classed as
	NO000256	J	Room (Room Z1/023)	very low risk and should
				be inspected every 12
40	Δ.	[] 4:1 -	7 0.15 1-1-1 4 01	months
46.	As NO000268	Floor tile	Z-Sub level 1 Store Room (Room Z1/023)	No Risk
47.	NO000208	Floor tile grey	Z-Sub level 1 Store	This item is classed as
		Thou are givey	Room (Room Z1/026)	very low risk and should
				be inspected every 12
				months
48.	As	Floor tile grey	Z-Sub level 1 Store	This item is classed as
	NO000275		Room (Room Z1/027)	very low risk and should be inspected every 12
				months
49.	NO000276	Debris/Residue	Z-Sub level 1 Store	No Risk
		broken boards	Room (Room Z1/027)	
50.	As	Ductwork joints	Z-Sub level 1 Store	This item is classed as
	NO000267		Room (Room Z1/027)	low risk and should be inspected every 6
				months
51.	NO000277	Fuses/flashguards	Z-Sub level 1 Store	No Risk
		inside fuses	Room (Room Z1/027)	
		discarded		
52.	NO000278	throughout  Debris/residue to	Z-Sub level 1 Store	No Risk
52.	140000270	floor	Room (Room Z1/027)	140 1 (131)
53.	NO000279	Debris/residue to	Z-Sub level 1 Store	Removed Sept 2023
		redundant	Room (Room Z1/027)	
F.4	Δ-	hangers/equipment	7 Oak Invol 4 Dt 1	This face to the state of
54.	As NO000267	Ductwork joints	Z-Sub level 1 Plant	This item is classed as
	140000207		Room (Room Z1/028)	very low risk and should be inspected every 12
				months
55.	NO000280	Ductwork joints	Z-Sub level 1 Store	This item should be
			Room (Room Z1/029)	removed by a licensed
EG	NOOOOOA	Duotusel isists	7 Cub lovel 4 Ct	contractor asap
56.	NO000281	Ductwork joints red/brown mastic	Z-Sub level 1 Store Room (Room Z1/029)	This item is classed as very low risk and should
		150/biowii iliasiic	1.00111 (1.00111 2 1/023)	be inspected every 12
				months
		1 =	7011 1401	N. B. I
57.	As NO000268	Floor tile	Z-Sub level 1 Store Room (Room Z1/029)	No Risk

		T.		
58.	NO000282	Debris/Residue to wall left of entrance	Z-Sub level 1 Boiler Room (Room Z1/030)	Removed Sept 2023
59.	NO000283	Debris/Residue to left wall	Z-Sub level 1 Boiler Room (Room Z1/030)	Removed Sept 2023
60.	NO000284	Ceiling Shuttering	Z-Sub level 1 Boiler Room (Room Z1/030)	This item is classed as very low risk and should be inspected every 12 months
61.	NO000285	Debris/Residue surrounding holes for flues	Z-Sub level 1 Boiler Room (Room Z1/030)	No Risk
62.	NO000286	Debris/Residue to rear RHS wall	Z-Sub level 1 Boiler Room (Room Z1/030)	Removed Sept 2023
63.	NO000287	Debris/Residue to floor	Z-Sub level 1 Boiler Room (Room Z1/030)	Removed Sept 2023
64.	NO000288	Debris/Residue to floor	Z-Sub level 1 Boiler Room (Room Z1/030)	No Risk
65.	NO000289	Floor tile	Z-Sub level 1 Boiler Room (Room Z1/030)	This item is classed as very low risk and should be inspected every 12 months
66.	As NO000268	Floor tile	Z-Sub level 1 Store Room (Room Z1/032)	No Risk
67.	As NO000271	Pipework gasket	Z-Sub level 1 Store Room (Room Z1/032)	This item is classed as very low risk and should be inspected every 12 months
68.	NO000290	Pipework wrap to pipe penetrations in ceiling	Z-Sub level 1 Store Room (Room Z1/032)	This item is classed as very low risk and should be inspected every 12 months
69.	As NO000251	Floor tile pink/grey including debris up the stairs	Z-Sub level 1 Stairwell Staircase (Room Z1/034)	No Risk
70.	NO000201	Floor tile red	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months
71.	NO000292	Floor tile grey	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months
72.	NO000293	Floor adhesive remnants	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months
73.	NO000294	Window putty/seal adjacent main entrance damaged and in-situ	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months
74.	NO000295	Debris/Residue to entrance porch, on top and to sides, including beneath shelf and framework	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months

				1
75.	NO000296	Debris/Residue to	Ground Floor Shop	Removed Sept 2023
		top of ceiling at	Floor Unit 1 (Room	
		entrance porch	G/001)	
76.	NO000297	Ceiling tile	Ground Floor Shop	No Risk
		including debris to	Floor Unit 1 (Room	
		floor	G/001)	
77.	NO000298	Wall coating, rear	Ground Floor Shop	No Risk
11.	140000290	wall beneath skim	Floor Unit 1 (Room	INO IXISK
		wali belleatii skiiii		
70	NOOOOOO	E1 (1)	G/001)	
78.	NO000299	Floor tile brown	Ground Floor Shop	This item is classed as
		surrounding	Floor Unit 1 (Room	very low risk and should
		columns	G/001)	be inspected every 12
				months
79.	NO000300	Debris/Residue	Ground Floor Shop	Removed Sept 2023
		surrounding feet of	Floor Unit 1 (Room	
		columns	G/001)	
80.	As	Debris/Residue	Ground Floor Shop	Removed Sept 2023
	NO000300	surrounding feet of	Floor Unit 1 (Room	
		columns	G/001)	
81.	NO000316	Floor nosing to	Ground Floor Shop	This item is classed as
5	1.0000010	stairs step up to	Floor Unit 1 (Room	very low risk and should
		window	G/001)	be inspected every 12
		VVIIIGOVV	3,501)	months
82.	As	Debris/Residue to	Ground Floor Porch Unit	Removed Sept 2023
02.				Removed Sept 2023
00	NO000295	floor	1 (Room G/002)	This it was in the country
83.	As	Ductwork joints	Ground Floor Porch Unit	This item is classed as
	NO000280		1 (Room G/002)	low risk and should be
				inspected every 6
				months
84.	As	Floor adhesive	Ground Floor Store	This item is classed as
	NO000293	remnants	Room Unit 1 (Room	very low risk and should
			G/003)	be inspected every 12
				months
85.	As	Floor adhesive	Ground Floor Store	This item is classed as
	NO000293	remnants	Room Unit 1 (Room	very low risk and should
			G/004)	be inspected every 12
			,	months
86.	NO000303	Floor tile	Ground Floor Store	This item is classed as
00.	11000000	grey/beige beneath	Room Bike Store (Room	very low risk and should
		modern lino	G/005)	be inspected every 12
		modern into	<i></i>	months
87.	NO000304	Ceiling shuttering	Ground Floor Store	No Risk
07.	NO000304	Ceiling shuttering		INO RISK
			Room Bike Store (Room	
			CIONE	
00		T1	G/005)	This there is a
88.	As	Tile grey/beige	Ground Floor Laboratory	This item is classed as
88.	As NO000303	Tile grey/beige beneath carpet		very low risk and should
88.			Ground Floor Laboratory	very low risk and should be inspected every 12
	NO000303	beneath carpet	Ground Floor Laboratory (Room G/007)	very low risk and should be inspected every 12 months
88. 89.	NO000303 As	beneath carpet  Tile grey/beige	Ground Floor Laboratory (Room G/007)	very low risk and should be inspected every 12 months  This item is classed as
	NO000303	beneath carpet	Ground Floor Laboratory (Room G/007)	very low risk and should be inspected every 12 months
	NO000303 As	beneath carpet  Tile grey/beige	Ground Floor Laboratory (Room G/007)	very low risk and should be inspected every 12 months  This item is classed as
	NO000303 As	beneath carpet  Tile grey/beige beneath modern	Ground Floor Laboratory (Room G/007)  Ground Floor Hallway/passageway	very low risk and should be inspected every 12 months This item is classed as very low risk and should
	NO000303 As	Tile grey/beige beneath modern lino	Ground Floor Laboratory (Room G/007)  Ground Floor Hallway/passageway Switch Room (Room	very low risk and should be inspected every 12 months  This item is classed as very low risk and should be inspected every 12
89.	NO000303 As NO000303	beneath carpet  Tile grey/beige beneath modern	Ground Floor Laboratory (Room G/007)  Ground Floor Hallway/passageway Switch Room (Room G/008) Ground Floor	very low risk and should be inspected every 12 months  This item is classed as very low risk and should be inspected every 12 months
89.	NO000303 As NO000303	Tile grey/beige beneath modern lino	Ground Floor Laboratory (Room G/007)  Ground Floor Hallway/passageway Switch Room (Room G/008)  Ground Floor Hallway/passageway	very low risk and should be inspected every 12 months  This item is classed as very low risk and should be inspected every 12 months
89.	NO000303 As NO000303	Tile grey/beige beneath modern lino	Ground Floor Laboratory (Room G/007)  Ground Floor Hallway/passageway Switch Room (Room G/008)  Ground Floor Hallway/passageway Switch Room (Room Gom G/008)	very low risk and should be inspected every 12 months  This item is classed as very low risk and should be inspected every 12 months
89.	NO000303 As NO000303	Tile grey/beige beneath modern lino	Ground Floor Laboratory (Room G/007)  Ground Floor Hallway/passageway Switch Room (Room G/008)  Ground Floor Hallway/passageway	very low risk and should be inspected every 12 months  This item is classed as very low risk and should be inspected every 12 months

	NO000254	insulation	Room behind lifts (Room	
	110000204	inodiation	G/009)	
92.	NO000306	Floor jointing	Ground Floor Switch	No Risk
		compound	Room behind lifts (Room G/009)	
93.	NO000307	Floor adhesive	Ground Floor	No Risk
		remnants beneath	Hallway/passageway lift	
94.	NO000308	carpet Debris/Residue to	lobby (Room G/010) Ground Floor	No Risk
J4.	140000000	wall, mid landing	Staircase/Stairwell	Norwisk
		, 3	(Room G/012)	
95.	NO000309	Debris/Residue	Ground Floor	Removed Sept 2023
			Staircase/Stairwell (Room G/014)	
96.	As	Floor tile	Ground Floor	This item is classed as
	NO000303	grey/beige within	Staircase/Stairwell	very low risk and should
		electrical boxing to wall cavity and	(Room G/014)	be inspected every 12 months
		floor		onaio
97.	As	Floor jointing	Ground Floor	No Risk
	NO000306	compound	Staircase/Stairwell	
00	٨٥	Floor tile	(Room G/014)	This item is classed as
98.	As NO000303	grey/beige carpet	Ground Floor Office (Room G/015)	very low risk and should
	140000303	grey/beige carpet	(100111 6/013)	be inspected every 12
				months
99.	As	Floor jointing	Ground Floor Store	No Risk
100	NO000306	compound	Room (Room G/017)	
100.	NO000310	Pipework insulation in wall	Ground Floor Store	This item is classed as low risk and should be
		penetration	Room (Room G/017)	inspected every 6
		periouduon		months
101.	As	Floor adhesive	Ground Floor Store	No Risk
	NO000307	remnants	Room (Room G/017)	
102.	As	Floor tile	Ground Floor Store	This item is classed as
	NO000303	grey/beige carpet	Room (Room G/017)	very low risk and should be inspected every 12
				months
103.	NO000311	Wall to nail/screw	Ground Floor Store	No Risk
		heads, various	Room (Room G/017)	
404		points on column	0 15' 0'	N. D'.
104.	As	Floor jointing	Ground Floor Store	No Risk
	NO000306	compound	Room unit 4 (Room G/018)	
105.	As	Floor adhesive	Ground Floor Store	No Risk
	NO000307	remnants	Room unit 4 (Room	
125	NOCCCC		G/018)	
106.	NO000312	Pipework	Ground Floor Store	This item should be
		insulation packing to former wall	Room unit 4 (Room G/018)	removed by a licensed contractor asap
		penetration	5/010)	σοπιασίοι ασαρ
107.	NO000313	Residue/Debris to	Ground Floor Store	Removed Sept 2023
		floor	Room unit 4 (Room	
1.5.5			G/018)	
108.	As	Floor jointing	Ground Floor Store	No Risk
109.	NO000306 As	compound Floor adhesive	Room (Room G/020) Ground Floor Store	No Risk
100.	, 10	1 loor danesive	Crodita Filodi Otore	TTO I CIOIC

	NO000307	remnants	Room (Room G/020)	
110.	As	Cabling braiding	Ground Floor Store	No Risk
	NO000301	insulation	Room (Room G/020)	
111.	Presumed	Pipework gasket	Ground Floor Unit 3	This item is classed as
		too deeply	(café) limited inspection	very low risk and should
		recessed to	to ceiling (Room G/022)	be inspected every 12
		sample	,	months
112.	As	Wall to nail/screw	Ground Floor Unit 3	No Risk
	NO000311	heads various	(café) limited inspection	
		points on column	to ceiling (Room G/022)	
113.	As	Floor adhesive	Ground Floor Unit 3	No Risk
	NO000307	remnants	(café) limited inspection	
			to ceiling (Room G/022)	
114.	As	Floor tile remnants	Ground Floor Unit 3	This item is classed as
	NO000303		(café) limited inspection	very low risk and should
			to ceiling (Room G/022)	be inspected every 12
				months
115.	As	Floor adhesive	Ground Floor Shop	No Risk
	NO000307	remnants	Floor former store	
			entrance (Room G/023)	
116.	As	Floor tile remnants	Ground Floor Shop	This item is classed as
	NO000303		Floor former store	very low risk and should
			entrance (Room G/023)	be inspected every 12
				months
117.	NO000314	Debris/Residue to	Ground Floor Shop	Removed Sept 2023
		both floor voids	Floor former store	
		adjacent front	entrance (Room G/023)	
		doors also on roller shutter		
118.	As	Floor adhesive	Ground Floor Office	No Risk
	NO000307	remnants	(Room G/026)	
119.	As	Floor adhesive	Ground Floor	No Risk
	NO000307	remnants	Hallway/passageway	
			(Room G/027)	
120.	As	Floor adhesive	Ground Floor	No Risk
	NO000307	remnants	Hallway/passageway	
			(Room G/028)	
121.	NO000315	Ceiling tiles	Ground Floor Bin store	No Risk
			(Room G/031)	
122.	As	Floor adhesive	Ground Floor Bin store	No Risk
	NO000307	remnants	(Room G/031)	
123.	As	Ceiling tiles	Ground Floor Store	No Risk
	L NICOCOCAE		Doom (Doom C/022)	
	NO000315		Room (Room G/032)	
124.	As	Floor adhesive	Ground Floor Store	No Risk
	As NO000307	remnants	Ground Floor Store Room (Room G/032)	
124. 125.	As NO000307 As	remnants Floor adhesive	Ground Floor Store Room (Room G/032) Ground Floor Staff	No Risk
125.	As NO000307 As NO000307	remnants Floor adhesive remnants	Ground Floor Store Room (Room G/032) Ground Floor Staff Room (Room G/035)	No Risk
	As NO000307 As NO000307 As	remnants Floor adhesive remnants Floor adhesive	Ground Floor Store Room (Room G/032) Ground Floor Staff Room (Room G/035) Ground Floor Office	
125. 126.	As NO000307 As NO000307 As NO000307	remnants Floor adhesive remnants Floor adhesive remnants	Ground Floor Store Room (Room G/032) Ground Floor Staff Room (Room G/035) Ground Floor Office (Room G/036)	No Risk
125.	As NO000307 As NO000307 As NO000307 As	remnants Floor adhesive remnants Floor adhesive remnants Floor adhesive	Ground Floor Store Room (Room G/032) Ground Floor Staff Room (Room G/035) Ground Floor Office (Room G/036) Ground Floor Entrance	No Risk
125. 126.	As NO000307 As NO000307 As NO000307	remnants Floor adhesive remnants Floor adhesive remnants	Ground Floor Store Room (Room G/032) Ground Floor Staff Room (Room G/035) Ground Floor Office (Room G/036) Ground Floor Entrance Hall/Foyer/Lobby	No Risk
125. 126. 127.	As NO000307 As NO000307 As NO000307	remnants Floor adhesive remnants Floor adhesive remnants Floor adhesive remnants	Ground Floor Store Room (Room G/032) Ground Floor Staff Room (Room G/035) Ground Floor Office (Room G/036) Ground Floor Entrance Hall/Foyer/Lobby (Room G/037)	No Risk  No Risk  No Risk
125. 126.	As NO000307 As NO000307 As NO000307 As	remnants Floor adhesive remnants Floor adhesive remnants Floor adhesive remnants Floor adhesive	Ground Floor Store Room (Room G/032) Ground Floor Staff Room (Room G/035) Ground Floor Office (Room G/036) Ground Floor Entrance Hall/Foyer/Lobby (Room G/037) Ground Floor	No Risk
125. 126. 127.	As NO000307 As NO000307 As NO000307	remnants Floor adhesive remnants Floor adhesive remnants Floor adhesive remnants	Ground Floor Store Room (Room G/032) Ground Floor Staff Room (Room G/035) Ground Floor Office (Room G/036) Ground Floor Entrance Hall/Foyer/Lobby (Room G/037) Ground Floor Hallway/Passageway	No Risk  No Risk  No Risk
125. 126. 127.	As NO000307 As NO000307 As NO000307 As	remnants Floor adhesive remnants Floor adhesive remnants Floor adhesive remnants Floor adhesive	Ground Floor Store Room (Room G/032) Ground Floor Staff Room (Room G/035) Ground Floor Office (Room G/036) Ground Floor Entrance Hall/Foyer/Lobby (Room G/037) Ground Floor	No Risk  No Risk  No Risk

	T	shop floor and	Staircase/Stairwell	vory low rick and should
		shop floor and understairs area	(Room G/039)	very low risk and should be inspected every 12 months
130.	As NO000307	Floor adhesive remnants	Ground Floor Staircase/Stairwell (Room G/039)	No Risk
131.	NO000318	Wall – within hole in wall under stairs	Ground Floor Staircase/Stairwell (Room G/039)	No Risk
132.	NO000319	Window putty/seal to discarded window	Ground Floor Staircase/Stairwell (Room G/039)	This item is classed as very low risk and should be inspected every 12 months
133.	NO000320	Floor tile	First Floor Plant Room (Room 1/005)	No Risk
134.	NO000321	Floor tile beneath carpet	Second Floor Landing including stairs up (Room 2/001)	No Risk
135.	NO000321	Floor tile beneath carpet	Second Floor Landing (Room 2/003)	No Risk
136.	As NO000320	Floor tile	Second Floor Plant Room (Room 2/004)	No Risk
137.	NO000322	Wall Coating	Second Floor Plant Room (Room 2/004)	No Risk
138.	NO000323	Wall void cavity	Second Floor Plant Room (Room 2/004)	No Risk
139.	NO000324	Ceiling void insulation top Of ceiling heater	Second Floor Hallway/passageway (Room 2/010)	No Risk
140.	As NO000321	Floor tile beneath carpet	Second Floor Hallway/passageway (Room 2/013)	No Risk
141.	NO000325	Debris/Residue to stairs	Second Floor Fire escape (Room 2/015)	Removed Sept 2023
142.	NO000326	Debris/Residue to side stairs (external wall) including sloping runner	Second Floor Fire escape (Room 2/015)	Removed Sept 2023
143.	NO000327	Floor nosing to stairs	Second Floor Fire escape (Room 2/015)	This item is classed as very low risk and should be inspected every 12 months
144.	As NO000321	Floor tile beneath carpet	Second Floor Hallway/passageway (Room 2/016)	No Risk
145.	As NO000321	Floor tile beneath carpet	Second Floor Hallway/passageway (Room 2/017)	No Risk
146.	As NO000321	Floor tile beneath carpet	Second Floor Store Room (Room 2/018)	No Risk
147.	NO000328	Pipework lining to insulation remnants	Second Floor Store Room (Room 2/018)	Removed Sept 2023
148.	NO000330	Window/putty seal from removed window	Second Floor Store Room (Room 2/018)	This item is classed as very low risk and should be inspected every 12

				months
149.	As NO000321	Floor tile beneath carpet	Second Floor Store Room Former toilets (Room 2/019)	No Risk
150.	NO000329	Ductwork	Second Floor Store Room Former toilets (Room 2/019)	This item is classed as very low risk and should be inspected every 12 months
151.	NO000331	Ceiling void ceiling above panel	Third Floor Landing (Room 3/001)	This item is classed as low risk and should be inspected every 6 months
152.	NO000332	Wall tile	Third Floor Plant Room (Room 3/004)	No Risk
153.	NO000333	Debris/Residue to stairs	Third Floor Fire Escape (Room 3/016)	This item is classed as low risk and should be inspected every 6 months
154.	NO000334	Ceiling sloping Packing to girders	Third Floor Fire Escape (Room 3/016)	No Risk
155.	NO000328	Pipework lining to insulation remnants to 2 large pipes and floor	Third Floor Store Room (Room 3/021)	Removed Sept 2023
156.	Presumed	Pipework gaskets	Third Floor Store Room (Room 3/021)	This item is classed as very low risk and should be inspected every 12 months
157.	Presumed	Pipework gaskets too deeply recessed to sample	Third Floor Store Room (Room 3/023)	This item is classed as very low risk and should be inspected every 12 months
158.	As NO000335	Beam cladding suspected continuation from electric cupboard	Fourth Floor Landing (Room 4/001)	This item is classed as very low risk and should be inspected every 12 months
159.	As NO000335	Beam cladding beneath skim, sampled via pre- existing damage to skim	Fourth Floor Electric cupboard (Room 4/002)	This item should be removed by a licensed contractor asap
160.	NO000336	Beam cladding remnants beneath girder	Fourth Floor Hub/Network Room (Room 4/006)	This item is classed as very low risk and should be inspected every 12 months
161.	NO000337	Debris/Reside to steel girder	Fourth Floor Hub/Network Room (Room 4/006)	Removed Sept 2023
162.	NO000338	Debris/Resdue	Fourth Floor Hub/Network Room (Room 4/006)	No Risk
163.	As NO000336	Beam cladding remnants beneath girder	Fourth Floor Plant Room (Room 4/007)	Removed Sept 2023
164.	As NO000337	Debris/Reside to steel girder	Fourth Floor Plant Room (Room 4/007)	Removed Sept 2023

	Τ.	T = /= .		
165.	As	Debris/Resdue	Fourth Floor Plant Room	No Risk
	NO000338		(Room 4/007)	
166.	NO000339	Tank pacing to	Fourth Floor Plant Room	No Risk
		brackets	(Room 4/007)	
167.	NO000340	Damp proof course	Fourth Floor Plant Room	No Risk
107.	140000040	surrounding	(Room 4/007)	140 I Clore
		windows	(100111 47001)	
400	NOOOOAA		E and Eland 199	This is the second of the seco
168.	NO000341	Fuses/flashguards	Fourth Floor Lift	This item is classed as
			Machinery Room (Room	very low risk and should
			4/008)	be inspected every 12
				months
169.	NO000342	Fuses/flashguards	Fourth Floor Lift	This item is classed as
		isolation strips	Machinery Room (Room	very low risk and should
		'	4/008)	be inspected every 12
			., 555)	months
170.	NO000373	Roof felt remnants	Fourth Floor Fire escape	No Risk
170.	110000373			INO ICISK
		to concrete	(Room 4/058)	
474	1100000074	144 H C 4	E	<del>-</del> 1
171.	NO000374	Wall coating to	Fourth Floor External	This item is classed as
		upper metal	roof area (Room 4/059)	very low risk and should
		cladding		be inspected every 12
				months
172.	Presumed	Pipework gaskets	Mezzanine Switch Room	This item is classed as
		to sprinkler system	midway between	very low risk and should
		to oprimite dystem	basement and ground	be inspected every 12
			floor	months
173.	NG001611	Wall panal		HIGHTIS
173.	NGUUTOTT	Wall panel	Ground Floor, Laundry	Na Dial.
			(Room G/001)	No Risk
174.	NG001612	Floor tile (with	Ground Floor, Laundry	This item is classed as
		adhesive) grey	(Room G/001)	low risk and should be
		beneath carpet		inspected every 6
				months
175.	NG001609	Wall panel	Ground Floor, Entrance	
		·	Hall/Foyer/Lobby Main	
			lift lobby (Room G/002)	No Risk
176.	NG001616	Ceiling	Ground Floor, Entrance	THE THER
170.	140001010	Cenning	Hall/Foyer/Lobby Main	
				No Diek
477	Λ -	\\\/-!! !	lift lobby (Room G/002)	No Risk
177.	As	Wall panel	First Floor, Entrance	
	NG001609		Hall/Foyer/Lobby Main	
			lift lobby (Room 1/001)	No Risk
178.	As	Ceiling	First Floor, Entrance	
	NG001616		Hall/Foyer/Lobby Main	
			lift lobby (Room 1/001)	No Risk
179.	As	Wall panel	First Floor, Entrance	
	NG001609	,	Hall/Foyer/Lobby next to	
	110001000		northerly fire exit (Room	
			1/002)	No Piek
400	٨٥	\/\all_n =1		No Risk
180.	As	Wall panel	Staircase/Stairwell	N. B. I
	NG001602		(Room 1/003)	No Risk
181.	As	Floor tile (with	Staircase/Stairwell	
	NG001603	adhesive) red	(Room 1/003)	No Risk
182.	As	Floor covering	Staircase/Stairwell	
	NG001604		(Room 1/003)	No Risk
183.	NG001610	Wall panel	Corridor west corridor	
. 55.	110001010	Trail parior	(Room 1/004)	No Risk
			( 1 ( O O I I I I I I O O T )	110 1 (101)
184.	As	Ceiling	Corridor west corridor	No Risk

	NG001616		(Room 1/004)	
185.	As	Wall panel	Staircase/Stairwell	
100.	NG001610	Trail parior	(Room 1/005)	No Risk
186.	As	Wall panel	Bedroom 130 (Room	THE PRIOR
100.	NG001602	VVali parioi	1/006)	No Risk
187.	As	Wall panel	Bedroom 214 (Room	TWO TRISIC
107.	NG001596	vvali pariei	1/007)	No Risk
188.	NG001590	Wall panel	Entrance	NOTISK
100.	140001000	vvali pariei	Hall/Foyer/Lobby Lift	
			lobby east (Room 2/001)	No Diek
400	NC004600	Mallmanal	Staircase/Stairwell North	No Risk
189.	NG001602	Wall panel		No Diek
400	NOOOAOOO	F1	fire exit (Room 2/002)	No Risk
190.	NG001603	Floor tile with	Staircase/Stairwell North	N. B. I
404	110001001	adhesive (red)	fire exit (Room 2/002)	No Risk
191.	NG001604	Floor covering	Staircase/Stairwell North	
			fire exit (Room 2/002)	No Risk
192.	As	Wall panel	Hallway/passageway	
	NG001602		Passage to Northerly fire	
			exit (Room 2/003)	No Risk
193.	As	Wall panel	Bedroom 230 (Room	
	NG001602		2/004)	No Risk
194.	NG001605	Wall panel	Corridor East Corridor	
		·	(Room 2/005)	No Risk
195.	NG001613	Ceiling	Corridor East Corridor	
			(Room 2/005)	No Risk
196.	NG001606	Wall panel	Staircase/Stairwell	
			(Room 2/006)	No Risk
197.	As	Wall panel	Kitchen adjacent service	
	NG001606	Trail parior	cupboard (Room 2/007)	No Risk
198.	NG001607	Wall panel	Entrance	TTO THOR
130.	140001007	vvali parici	Hall/Foyer/Lobby Lobby	
			to emergency exit	
			(Room 2/008)	No Risk
199.	NG001608	Wall coating	Staircase/Stairwell	TWO TRISIC
133.	140001000	vvaii coating	Emergency fire exit	
			(Room 2/009)	No Risk
200.	As	Wall panel	Bedroom 214 (Room	INO INISK
200.	NG001596	vvali pariei	2/010)	No Diek
204		Cailing		No Risk
201.	As	Ceiling	Corridor West corridor	NI. Dist
000	NG001613	\ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \	(Room 2/011)	No Risk
202.	NG001594	Wall panel	Staircase/Stairwell fire	
			exit staircase (Room	
			3/001)	No Risk
203.	NG001595	Floor tile with	Staircase/Stairwell fire	
		adhesive	exit staircase (Room	
			3/001)	No Risk
204.	NG001596	Wall panel	Corridor East Corridor	
			(Room 3/002)	No Risk
205.	NG001614	Ceiling coating	Corridor East Corridor	
			(Room 3/002)	No Risk
206.	As	Floor tile with	Hallway/Passageway	
	NG001595	adhesive	(Room 3/003)	No Risk
207.	NG001597	Wall panel	Staircase/Stairwell	
			South stairwell (Room	
			3/004)	No Risk
208.	NG001598	Wall panel	Entrance	No Risk
200.	140001390	vvali parici	Littratioe	TAO I VISIV

			T	
			Hall/Foyer/Lobby (Room 3/005)	
209.	NG001599	Wall panel	Staircase/Stairwell (Room 3/006)	No Risk
210.	As NG001599	Wall panel	Plant Room (Room 3/007)	No Risk
211.	NG001601	Wall panel	Bedroom 306 (Room 3/008)	No Risk
212.	As NG001602	Wall coating	Bedroom 330 (Room 3/009)	No Risk
213.	As NG001596	Wall panel	Corridor West Corridor (Room 3/010)	No Risk
214.	As NG001614	Ceiling coating	Corridor West Corridor (Room 3/010)	No Risk
215.	NG001588	Wall coating to brickwork	Entrance Hall/Foyer/Lobby (Room 4/001)	No Risk
216.	NG001589	Wall panel	Entrance Hall/Foyer/Lobby (Room 4/001)	No Risk
217.	NG001590	Wall panel	Bedroom 401 (Room 4/002)	No Risk
218.	NG001591	Wall panel	Bedroom 405 (Room 4/003)	No Risk
219.	NG001592	Wall panel	Corridor (Room 4/004)	No Risk
220.	NG001593	Wall coating	Stairs/Hall Landing Roof	This item is classed as
		205	accessed (Room 4/005)	low risk and should be inspected every 6 months
221.	NG001615	Ceiling	Corridor (Room 4/006)	No Risk
222.	AW005669	Floor covering	Rear stairwell adjacent Rm 301 (Room 2/001)	No Risk
223.	AW005670	Ceiling void – residue to redundant radiator	Corridor adjacent Rm 214 (Room 2/002)	No Risk
224.	AW005671	Ceiling void – paint coating to ceiling	Corridor adjacent Rm 316 (Room 3/001)	No Risk
225.	NZ001414	Debris/Residue to ceiling floor below	Loft space within lift lobby (Room 1/001)	No Risk
226.	As NZ001414	Debris/Residue to ceiling floor below	Loft space within crazy lobby (Room 1/002)	No Risk
227.	NZ001415	Debris/Residue to ceiling floor below	Loft space within corridors to flats 106-111 (Room 1/003)	No Risk
228.	As NZ001415	Debris/Residue to ceiling floor below	Loft space within corridor adjacent flat 110 (Room 1/004)	No Risk
229.	NZ001416	Debris/Residue to ceiling floor below	Loft space within corridors to flats 112-119 (Room 1/005)	No Risk
230.	As NZ001416	Debris/Residue to ceiling floor below	Loft space within corridors to flats 120-125 (Room 1/006)	No Risk
231.	NZ001417	Debris/Residue to ceiling floor below	Loft space within corridors to flats 126-130 (Room 1/007)	No Risk

232.	As	Debris/Residue to	Loft space within	
	NZ001417	ceiling floor below	corridor adjacent flat 130	
			(Room 1/008)	No Risk
233.	NZ001418	Debris/Residue to	Loft space within	
		ceiling floor below	corridors to flats 101-	
			103 (Room 1/009)	No Risk
234.	As	Debris/Residue to	Loft space within	
	NZ001418	ceiling floor below	corridors to flats 104-	
		coming moon wonern	105 (Room 1/010)	No Risk
235.	NZ001408	Debris/Residue to	Loft space within lift	
200.	112001100	ceiling floor below	lobby (Room 2/001)	No Risk
236.	As	Debris/Residue to	Loft space within gaming	TVOTAISIC
230.	NZ001408	ceiling floor below	room lobby (Room	
	112001400	ceiling noor below		No Risk
227	N7004400	Dahria/Dasidus ta	2/002)	INO KISK
237.	NZ001409	Debris/Residue to	Loft space within	
		ceiling floor below	corridor to flats 207-208	
			(Room 2/003)	No Risk
238.	As	Debris/Residue to	Loft space within	
	NZ001409	ceiling floor below	corridor to flats 209-211	
			(Room 2/004)	No Risk
239.	NZ001410	Debris/Residue to	Loft space within	
		ceiling floor below	corridor adjacent flat 210	
			(Room 2/005)	No Risk
240.	As	Debris/Residue to	Loft space within	
	NZ001410	ceiling floor below	corridor to flats 212-219	
			(Room 2/006)	No Risk
241.	NZ001411	Debris/Residue to	Loft space within	
		ceiling floor below	corridor to flats 220-225	
		9	(Room 2/007)	No Risk
242.	As	Debris/Residue to	Loft space within	TTO THOM
272.	NZ001411	ceiling floor below	corridor adjacent lift	
	142001411	centrig fleet belew	lobby (Room 2/008)	No Risk
243.	NZ001412	Debris/Residue to	Loft space within	TVO TCISIC
243.	112001412	ceiling floor below	corridor to flats 226-230	
		celling floor below	(Room 2/009)	No Biok
244.	Λ -	D =	,	No Risk
244.	As	Debris/Residue to	Loft space within	
	NZ001412	ceiling floor below	corridor adjacent flat 230	N. D. I
			(Room 2/010)	No Risk
245.	NZ001413	Debris/Residue to	Loft space within	
		ceiling floor below	corridor to flats 201-203	
			(Room 2/011)	No Risk
246.	As	Debris/Residue to	Loft space within	
	NZ001413	ceiling floor below	corridor to flats 204-205	
			(Room 2/012)	No Risk
247.	NZ001403	Debris/Residue to	Loft space within lobby	
		ceiling floor below	(Room 3/001)	No Risk
248.	As	Debris/Residue to	Loft space within football	
	NZ001403	ceiling floor below	pool room lobby (Room	
			3/002)	No Risk
249.	NZ001404	Debris/Residue to	Loft space within	
		ceiling floor below	corridor to flats 306-311	
		251111g 11301 D010W	(Room 3/003)	No Risk
250.	As	Debris/Residue to	Loft space within	110 THOR
230.	NZ001404	ceiling floor below	corridor adjacent Flat	
	112001404	cening noor below		No Risk
251	N7001405	Dobrie/Posidue to	311 (Room 3/004)	INOTAIN
251.	NZ001405	Debris/Residue to	Loft space within	No Diek
		ceiling floor below	corridor to flats 312-319	No Risk

			(Room 3/005)	
252.	As NZ001405	Debris/Residue to ceiling floor below	Loft space within corridor to flats 320-325 (Room 3/006)	No Risk
253.	As NZ001404	Debris/Residue to ceiling floor below	Loft space within corridor adjacent Flat 321 (Room 3/007)	No Risk
254.	NZ001406	Debris/Residue to ceiling floor below	Loft space within corridor to flats 326-330 (Room 3/008)	No Risk
255.	As NZ001406	Debris/Residue to ceiling floor below	Loft space within corridor adjacent flat 330 (Room 3/009)	No Risk
256.	NZ001407	Debris/Residue to ceiling floor below	Loft space within corridor to flats 301-304 (Room 3/010)	No Risk
257.	As NZ001407	Debris/Residue to ceiling floor below	Loft space within corridor to flats 301-304 (Room 3/011)	No Risk
258.	NZ001401	Debris/Residue to ceiling floor below	Loft space within corridor to flats 413-414 (Room 4/001)	No Risk
259.	As NZ001401	Debris/Residue to ceiling floor below	Loft space within corridor to flats 408-412 (Room 4/002)	No Risk
260.	NZ001402	Debris/Residue to ceiling floor below	Loft space within corridor to flats 415-416 (Room 4/003)	No Risk
261.	As NZ001402	Debris/Residue to ceiling floor below	Loft space within corridor to flats 403-407 (Room 4/004)	No Risk
262.	EV005969	Textured coated wall & debris to ceiling loft space where the wall had been damaged to ducting installation	Loft space/Ceiling void (R/01)	No Risk

Please note the survey carried out was non-intrusive and any areas not listed above may not have been accessed or had samples taken, should major refurbishment be planned for the property, further investigation will be required.

#### **Photographs of Areas Sampled**



4.	Presumed	Pipework Gaskets to deeply recessed to sample	Z-Sub level 1 Shop Floor (Room Z1/001)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
			J	
5.	NO000254	Cable braiding insulation	Z-Sub level 1 Shop Floor (Room Z1/001)	Does not contain asbestos.
6.	NO000255	Cable braiding insulation	Z-Sub level 1 Shop Floor (Room Z1/001)	Does not contain asbestos.

7.	NO000256	Fuses flashguards	Z-Sub level 1 Shop Floor (Room Z1/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
		PLEASE PAY HERE		
8.	NO000257	Debris/Residue	Z-Sub level 1 Shop Floor (Room Z1/001)	Removed Sept 2023
G				
9.	NO000258	Debris/Residue from boiler room entrance across to stairs and adjacent areas	Z-Sub level 1 Shop Floor (Room Z1/001)	Removed Sept 2023

10.	NO000259	Debris/Residue to redundant pump	Z-Sub level 1 Shop Floor (Room Z1/001)	Does not contain asbestos.
11.	NO000264	Debris/Residue to floor adjacent stairwell	Z-Sub level 1 Shop Floor (Room Z1/001)	Removed Sept 2023
C				
12.	NO000266	Ceiling tile behind metal grid tiles	Z-Sub level 1 Shop Floor (Room Z1/001)	Does not contain asbestos.


13.	NO000267	Ductwork joints	Z-Sub level 1 Shop Floor (Room Z1/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
14.	NO000260	Floor tile on shelving	Z-Sub level 1 Store Room (Room Z1/006)	Does not contain asbestos.
15.	NO000261	Debris/Residue to redundant pipe hanger	Z-Sub level 1 Switch Room (Room Z1/007)	Removed Sept 2023

16.	As NO000254	Cable braiding insulation	Z-Sub level 1 Switch Room (Room Z1/007)	Does not contain asbestos.
17.	NO000256	Fuses flashguards	Z-Sub level 1 Switch Room (Room Z1/007)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
18.	NO000302	Door seal/gasket discarded on floor	Z-Sub level 1 Switch Room (Room Z1/007)	Does not contain asbestos.

19.	NO000262	Debris/residue to floor	Z-Sub level 1 Plant Room (Room Z1/008)	Removed Sept 2023
20.	NO000263	Ductwork joints	Z-Sub level 1 Plant Room (Room Z1/008)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
21.	As NO000263	Ductwork joints	Z-Sub level 1 Staircase/Stairwell (Room Z1/009)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
		TOTAL SECTION AND ADDRESS OF THE PARTY.		

22.	NO000265	Wall	Z-Sub level 1 Staircase/Stairwell (Room Z1/009)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.	
23.	As NO000265	Debris/Residue foot of stairwell and adjacent areas	Z-Sub level 1 Staircase/Stairwell (Room Z1/009)	Removed Sept 2023	
G					
24.	NO000301	Cable braiding insulation remnants to wall	Z-Sub level 1 Staircase/Stairwell (Room Z1/009)	Does not contain asbestos.	

25.	NO000268	Floor tile	Z-Sub level 1 Store Room (Room Z1/010)	Does not contain asbestos.
26.	NO000269	Floor jointing compound	Z-Sub level 1 Store Room (Room Z1/014)	Does not contain asbestos.
27.	As NO000269	Floor jointing compound	Z-Sub level 1 Store Room (Room Z1/017)	Does not contain asbestos.

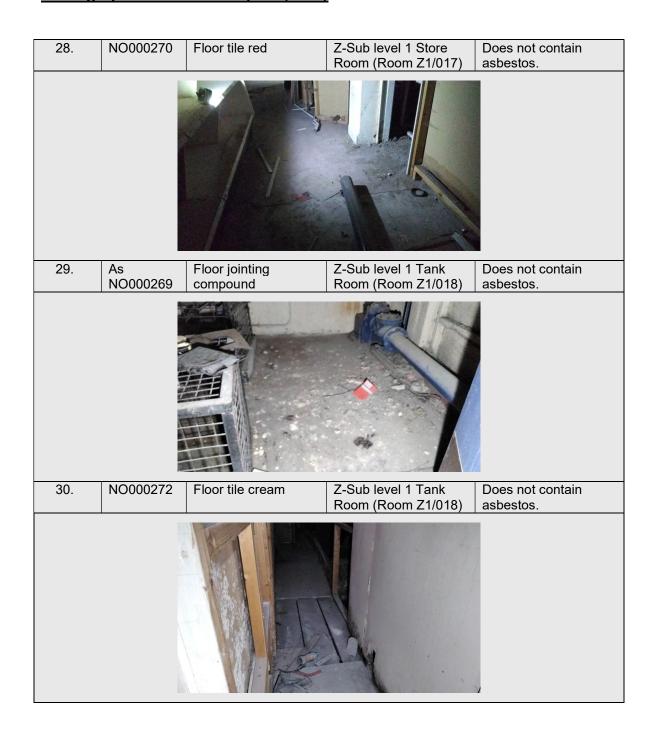

31.	As NO000256	Fuses/ flashguards	Z-Sub level 1 Tank Room (Room Z1/018)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
32.	NO000271	Pipework gaskets	Z-Sub level 1 Tank Room (Room Z1/018)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
33.	As NO000271	Pipework gaskets	Z-Sub level 1 Tank Room (Room Z1/018)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.

34.	NO000273	Debris/Residue	Z-Sub level 1 Tank Room (Room Z1/018)	Removed Sept 2023
35.	NO000274	Floor tile pink grey	Z-Sub level 1 Shop Floor (Room Z1/019)	Does not contain asbestos.
36.	Presumed	Pipework Gaskets to deeply recessed to sample	Z-Sub level 1 Shop Floor (Room Z1/019)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.

37.	As NO000257	Debris/Residue	Z-Sub level 1 Shop Floor (Room Z1/019)	Removed Sept 2023	
38.	As NO000266	Ceiling tile behind metal grid tiles	Z-Sub level 1 Shop Floor (Room Z1/019)	Does not contain asbestos.	
39.	As NO000272	Floor tile cream	Z-Sub level 1 Shop Floor (Room Z1/019)	Does not contain asbestos.	

40.	As NO000267	Ductwork joints	Z-Sub level 1 Shop Floor (Room Z1/019)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
41.	As NO000251	Floor tile pink/grey	Z-Sub level 1 Staircase/Stairwell (Room Z1/020)	Does not contain asbestos.
42.	As NO000273	Debris/Reside to ceiling void and floor below	Z-Sub level 1 Store Room (Room Z1/021)	Removed Sept 2023

43.	Presumed	Pipework Gaskets	Z-Sub level 1 Store Room (Room Z1/021)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
44.	As NO000254	Cable braiding/insulation	Z-Sub level 1 Store Room (Room Z1/022)	Does not contain asbestos.
45.	As NO000256	Fuses flashguards	Z-Sub level 1 Store Room (Room Z1/023)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.

46.	As NO000268	Floor tile	Z-Sub level 1 Store Room (Room Z1/023)	Does not contain asbestos.
47.	NO000275	Floor tile grey	Z-Sub level 1 Store Room (Room Z1/026)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
Ç				
48.	As NO000275	Floor tile grey	Z-Sub level 1 Store Room (Room Z1/027)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
Marghus Street, and the street				

49.	NO000276	Debris/Residue broken boards	Z-Sub level 1 Store Room (Room Z1/027)	Does not contain asbestos.
50.	As NO000267	Ductwork joints	Z-Sub level 1 Store Room (Room Z1/027)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
Ç				CI
51.	NO000277	Fuses/flashguards inside fuses discarded throughout	Z-Sub level 1 Store Room (Room Z1/027)	Does not contain asbestos.

52.	NO000278	Debris/residue to floor	Z-Sub level 1 Store Room (Room Z1/027)	Does not contain asbestos.
53.	NO000279	Debris/residue to redundant hangers/equipment	Z-Sub level 1 Store Room (Room Z1/027)	Removed Sept 2023
Ç				
54.	As NO000267	Ductwork joints	Z-Sub level 1 Plant Room (Room Z1/028)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.

55.	NO000280	Ductwork joints	Z-Sub level 1 Store Room (Room Z1/029)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
56.	NO000281	Ductwork joints red/brown mastic	Z-Sub level 1 Store Room (Room Z1/029)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
57.	As NO000268	Floor tile	Z-Sub level 1 Store Room (Room Z1/029)	Does not contain asbestos.

58.	NO000282	Debris/Residue to wall left of entrance	Z-Sub level 1 Boiler Room (Room Z1/030)	Removed Sept 2023
59.	NO000283	Debris/Residue to left wall	Z-Sub level 1 Boiler Room (Room Z1/030)	Removed Sept 2023
60.	NO000284	Ceiling Shuttering	Z-Sub level 1 Boiler Room (Room Z1/030)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.

61.	NO000285	Debris/Residue surrounding holes for flues	Z-Sub level 1 Boiler Room (Room Z1/030)	Does not contain asbestos.
62.	NO000286	Debris/Residue to rear RHS wall	Z-Sub level 1 Boiler Room (Room Z1/030)	Removed Sept 2023
	NOGOROZZ	Dokaja (Pasidua ta	T Sub local d Pailage	Damayard Sant 2000
63.	NO000287	Debris/Residue to floor	Z-Sub level 1 Boiler Room (Room Z1/030)	Removed Sept 2023

64.	NO000288	Debris/Residue to floor	Z-Sub level 1 Boiler Room (Room Z1/030)	Does not contain asbestos.
65.	NO000289	Floor tile	Z-Sub level 1 Boiler Room (Room Z1/030)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
66.	As NO000268	Floor tile	Z-Sub level 1 Store Room (Room Z1/032)	Does not contain asbestos.

67.	As NO000271	Pipework gasket	Z-Sub level 1 Store Room (Room Z1/032)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
68.	NO000290	Pipework wrap to pipe penetrations in ceiling	Z-Sub level 1 Store Room (Room Z1/032)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
69.	As NO000251	Floor tile pink/grey including debris up the stairs	Z-Sub level 1 Stairwell Staircase (Room Z1/034)	Does not contain asbestos.

70.	NO000201	Floor tile red	Ground Floor Shop Floor Unit 1 (Room G/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
71.	NO000292	Floor tile grey	Ground Floor Shop Floor Unit 1 (Room G/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
72.	NO000293	Floor adhesive remnants	Ground Floor Shop Floor Unit 1 (Room G/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.

	1			,
73.	NO000294	Window putty/seal adjacent main entrance damaged and in-situ	Ground Floor Shop Floor Unit 1 (Room G/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
74.	NO000295	Debris/Residue to entrance porch, on top and to sides, including beneath shelf and framework	Ground Floor Shop Floor Unit 1 (Room G/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
75.	NO000296	Debris/Residue to top of ceiling at entrance porch	Ground Floor Shop Floor Unit 1 (Room G/001)	Removed Sept 2023

76.	NO000297	Ceiling tile including debris to floor	Ground Floor Shop Floor Unit 1 (Room G/001)	Does not contain asbestos.
77.	NO000298	Wall coating, rear wall beneath skim	Ground Floor Shop Floor Unit 1 (Room G/001)	Does not contain asbestos.
78.	NO000299	Floor tile brown surrounding columns	Ground Floor Shop Floor Unit 1 (Room G/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.

79.	NO000300	Debris/Residue surrounding feet of columns	Ground Floor Shop Floor Unit 1 (Room G/001)	Removed Sept 2023
80.	As NO000300	Debris/Residue surrounding feet of columns	Ground Floor Shop Floor Unit 1 (Room G/001)	Removed Sept 2023
G	3U			Cili
81.	NO000316	Floor nosing to stairs step up to window	Ground Floor Shop Floor Unit 1 (Room G/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.

82.	As NO000295	Debris/Residue to floor	Ground Floor Porch Unit 1 (Room G/002)	Removed Sept 2023
83.	As NO000280	Ductwork joints	Ground Floor Porch Unit 1 (Room G/002)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
Ç			5	CI
84.	As NO000293	Floor adhesive remnants	Ground Floor Store Room Unit 1 (Room G/003)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.

85.	As NO000293	Floor adhesive remnants	Ground Floor Store Room Unit 1 (Room G/004)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
86.	NO000303	Floor tile grey/beige beneath modern lino	Ground Floor Store Room Bike Store (Room G/005)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
87.	NO000304	Ceiling shuttering	Ground Floor Store Room Bike Store (Room G/005)	Does not contain asbestos.

88.	As NO000303	Tile grey/beige beneath carpet	Ground Floor Laboratory (Room G/007)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
89.	As NO000303	Tile grey/beige beneath modern lino	Ground Floor Hallway/passageway Switch Room (Room G/008)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
90.	NO000305	Pipework Gasket	Ground Floor Hallway/passageway Switch Room (Room G/008)	Does not contain asbestos.

91.	As NO000254	Cable braiding insulation	Ground Floor Switch Room behind lifts (Room G/009)	Does not contain asbestos.
92.	NO000306	Floor jointing compound	Ground Floor Switch Room behind lifts (Room G/009)	Does not contain asbestos.
93.	NO000307	Floor adhesive remnants beneath carpet	Ground Floor Hallway/passageway lift lobby (Room G/010)	Does not contain asbestos.


94.	NO000308	Debris/Residue to wall, mid landing	Ground Floor Staircase/Stairwell (Room G/012)	Does not contain asbestos.		
95.	NO000309	Debris/Residue	Ground Floor Staircase/Stairwell (Room G/014)	Removed Sept 2023		
G						
96.	As NO000303	Floor tile grey/beige within electrical boxing to wall cavity and floor	Ground Floor Staircase/Stairwell (Room G/014)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.		

97.	As NO000306	Floor jointing compound	Ground Floor Staircase/Stairwell (Room G/014)	Does not contain asbestos.
98.	As NO000303	Floor tile grey/beige carpet	Ground Floor Office (Room G/015)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
99.	As NO000306	Floor jointing compound	Ground Floor Store Room (Room G/017)	Does not contain asbestos.

100.	NO000310	Pipework insulation in wall penetration	Ground Floor Store Room (Room G/017)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
101.	As NO000307	Floor adhesive remnants	Ground Floor Store Room (Room G/017)	Does not contain asbestos.
102.	As NO000303	Floor tile grey/beige carpet	Ground Floor Store Room (Room G/017)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.

103.	NO000311	Wall to nail/screw heads, various points on column	Ground Floor Store Room (Room G/017)	Does not contain asbestos.
104.	As NO000306	Floor jointing compound	Ground Floor Store Room unit 4 (Room G/018)	Does not contain asbestos.
105.	As NO000307	Floor adhesive remnants	Ground Floor Store Room unit 4 (Room G/018)	Does not contain asbestos.

106.	NO000312	Pipework insulation packing to former wall penetration	Ground Floor Store Room unit 4 (Room G/018)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
107.	NO000313	Residue/Debris to floor	Ground Floor Store Room unit 4 (Room G/018)	Removed Sept 2023
108.	As NO000306	Floor jointing compound	Ground Floor Store Room (Room G/020)	Does not contain asbestos.

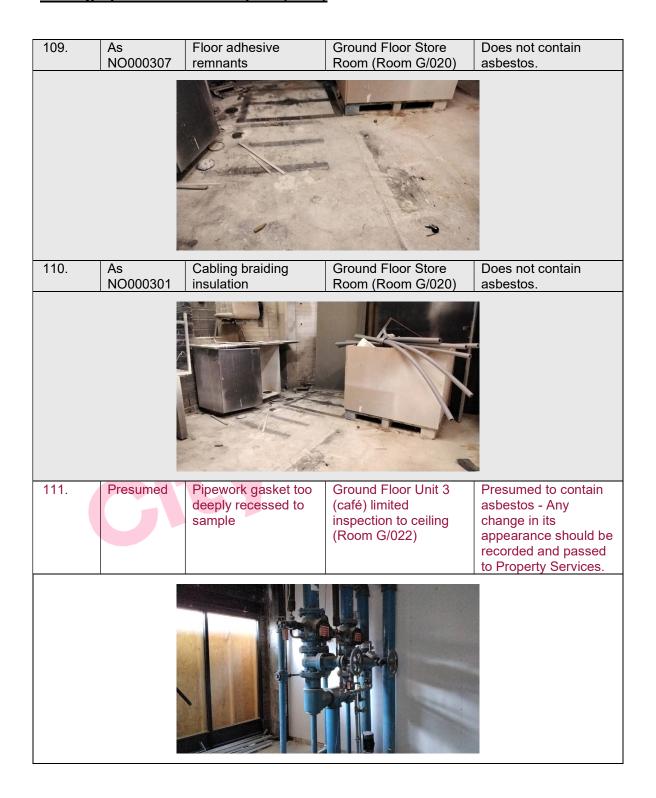

112.	As NO000311	Wall to nail/screw heads various points on column	Ground Floor Unit 3 (café) limited inspection to ceiling (Room G/022)	Does not contain asbestos.
113.	As NO000307	Floor adhesive remnants	Ground Floor Unit 3 (café) limited inspection to ceiling (Room G/022)	Does not contain asbestos.
114.	As NO000303	Floor tile remnants	Ground Floor Unit 3 (café) limited inspection to ceiling (Room G/022)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.

115.	As NO000307	Floor adhesive remnants	Ground Floor Shop Floor former store entrance (Room G/023)	Does not contain asbestos.
116.	As NO000303	Floor tile remnants	Ground Floor Shop Floor former store entrance (Room G/023)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
117.	NO000314	Debris/Residue to both floor voids adjacent front doors also on roller shutter	Ground Floor Shop Floor former store entrance (Room G/023)	Removed Sept 2023

118.	As NO000307	Floor adhesive remnants	Ground Floor Office (Room G/026)	Does not contain asbestos.
119.	As NO000307	Floor adhesive remnants	Ground Floor Hallway/passageway (Room G/027)	Does not contain asbestos.
120.	As NO000307	Floor adhesive remnants	Ground Floor Hallway/passageway (Room G/028)	Does not contain asbestos.


121.	NO000315	Ceiling tiles	Ground Floor Bin store (Room G/031)	Does not contain asbestos.
122.	As NO000307	Floor adhesive remnants	Ground Floor Bin store (Room G/031)	Does not contain asbestos.
123.	As NO000315	Ceiling tiles	Ground Floor Store Room (Room G/032)	Does not contain asbestos.

124.	As NO000307	Floor adhesive remnants	Ground Floor Store Room (Room G/032)	Does not contain asbestos.
125.	As NO000307	Floor adhesive remnants	Ground Floor Staff Room (Room G/035)	Does not contain asbestos.
126.	As NO000307	Floor adhesive remnants	Ground Floor Office (Room G/036)	Does not contain asbestos.

127.	As NO000307	Floor adhesive remnants	Ground Floor Entrance Hall/Foyer/Lobby (Room G/037)	Does not contain asbestos.
		Photo the second		
128.	As NO000307	Floor adhesive remnants	Ground Floor Hallway/Passageway (Room G/038)	Does not contain asbestos.
129.	NO000317	Floor tile to former shop floor and understairs area	Ground Floor Staircase/Stairwell (Room G/039)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.

130.	As NO000307	Floor adhesive remnants	Ground Floor Staircase/Stairwell (Room G/039)	Does not contain asbestos.
131.	NO000318	Wall – within hole in wall under stairs	Ground Floor Staircase/Stairwell (Room G/039)	Does not contain asbestos.
132.	NO000319	Window putty/seal to discarded window	Ground Floor Staircase/Stairwell (Room G/039)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.

133.	NO000320	Floor tile	First Floor Plant Room (Room 1/005)	Does not contain asbestos.				
	(Nooiii 17003) assestos.							
134.	NO000321	Floor tile beneath carpet	Second Floor Landing including stairs up (Room 2/001)	Does not contain asbestos.				
135.	NO000321	Floor tile beneath carpet	Second Floor Landing (Room 2/003)	Does not contain asbestos.				

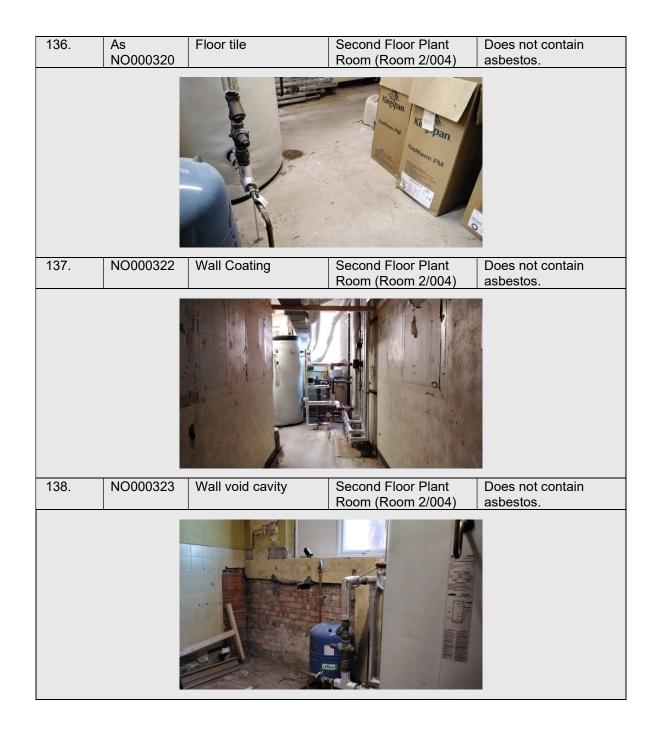

139.	NO000324	Ceiling void insulation top Of ceiling heater	Second Floor Hallway/passageway (Room 2/010)	Does not contain asbestos.
140.	As NO000321	Floor tile beneath carpet	Second Floor Hallway/passageway (Room 2/013)	Does not contain asbestos.
141.	NO000325	Debris/Residue to stairs	Second Floor Fire escape (Room 2/015)	Removed Sept 2023

142.	NO000326	Debris/Residue to side stairs (external wall) including sloping runner	Second Floor Fire escape (Room 2/015)	Removed Sept 2023
143.	NO000327	Floor nosing to stairs	Second Floor Fire escape (Room 2/015)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
G			2	
144.	As NO000321	Floor tile beneath carpet	Second Floor Hallway/passageway (Room 2/016)	Does not contain asbestos.

145.	As NO000321	Floor tile beneath carpet	Second Floor Hallway/passageway (Room 2/017)	Does not contain asbestos.
146.	As NO000321	Floor tile beneath carpet	Second Floor Store Room (Room 2/018)	Does not contain asbestos.
147.	NO000328	Pipework lining to insulation remnants	Second Floor Store Room (Room 2/018)	Removed Sept 2023

148.	NO000330	Window/putty seal from removed window	Second Floor Store Room (Room 2/018)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.		
149.	As NO000321	Floor tile beneath carpet	Second Floor Store Room Former toilets (Room 2/019)	Does not contain asbestos.		
150.	NO000329	Ductwork	Second Floor Store Room Former toilets (Room 2/019)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.		
STIPPITY OCIVIOCS.						

151.	NO000331	Ceiling void ceiling above panel	Third Floor Landing (Room 3/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
152.	NO000332	Wall tile	Third Floor Plant Room (Room 3/004)	Does not contain asbestos.
			35	
153.	NO000333	Debris/Residue to stairs	Third Floor Fire Escape (Room 3/016)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.

154.	NO000334	Ceiling sloping Packing to girders	Third Floor Fire Escape (Room 3/016)	Does not contain asbestos.		
155.	NO000328	Pipework lining to insulation remnants to 2 large pipes and floor	Third Floor Store Room (Room 3/021)	Removed Sept 2023		
G				CI		
156.	Presumed	Pipework gaskets	Third Floor Store Room (Room 3/021)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.		
	to Property Services.					

157.	Presumed	Pipework gaskets too deeply recessed to sample	Third Floor Store Room (Room 3/023)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
158.	As NO000335	Beam cladding suspected continuation from electric cupboard	Fourth Floor Landing (Room 4/001)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
G				
159.	As NO000335	Beam cladding beneath skim, sampled via pre- existing damage to skim	Fourth Floor Electric cupboard (Room 4/002)	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.

160.	NO000336	Beam cladding remnants beneath girder	Fourth Floor Hub/Network Room (Room 4/006)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
161.	NO000337	Debris/Reside to steel girder	Fourth Floor Hub/Network Room (Room 4/006)	Removed Sept 2023
162.	NO000338	Debris/Residue	Fourth Floor Hub/Network Room (Room 4/006)	Does not contain asbestos.

163.	As NO000336	Beam cladding remnants beneath girder	Fourth Floor Plant Room (Room 4/007)	Removed Sept 2023
164.	As NO000337	Debris/Reside to steel girder	Fourth Floor Plant Room (Room 4/007)	Removed Sept 2023
165.	As	Debris/Residue	Fourth Floor Plant	Does not contain
105.	NO000338	Deblis/Residue	Room (Room 4/007)	asbestos.


166.	NO000339	Tank pacing to brackets	Fourth Floor Plant Room (Room 4/007)	Does not contain asbestos.
167.	NO000340	Damp proof course surrounding windows	Fourth Floor Plant Room (Room 4/007)	Does not contain asbestos.
168.	NO000341	Fuses/flashguards	Fourth Floor Lift Machinery Room (Room 4/008)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.


169.	NO000342	Fuses/flashguards isolation strips	Fourth Floor Lift Machinery Room (Room 4/008)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
170.	NO000373	Roof felt remnants to concrete	Fourth Floor Fire escape (Room 4/058)	Does not contain asbestos.
171.	NO000374	Wall coating to upper metal cladding	Fourth Floor External roof area (Room 4/059)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.


172.	Presume	d Pipework gaskets sprinkler system	Room midway between basement and ground floor	Presumed to contain asbestos - Any change in its appearance should be recorded and passed to Property Services.
173.	NG001611	Wall panel	Ground Floor, Laundry (Room G/001)	Does not contain asbestos.
474	NCOOACAD		Crewal Floor Lawrence	Contains selected Any
174.	NG001612	Floor tile (with adhesive) grey beneath carpet	Ground Floor, Laundry (Room G/001)	Contains asbestos - Any change in its appearance should be recorded and passed to Property Services.
		No.		

175.	NG001609	Wall panel	Ground Floor, Entrance Hall/Foyer/Lobby Main lift lobby (Room G/002)	Does not contain asbestos.
		4		
176.	NG001616	Ceiling	Ground Floor, Entrance Hall/Foyer/Lobby Main lift lobby (Room G/002)	Does not contain asbestos.
177.	As NG001609	Wall panel	First Floor, Entrance Hall/Foyer/Lobby Main lift lobby (Room 1/001)	Does not contain asbestos.
		200		

178.	As NG001616	Ceiling	First Floor, Entrance Hall/Foyer/Lobby Main lift lobby (Room 1/001)	Does not contain asbestos.
179.	As NG001609	Wall panel	First Floor, Entrance Hall/Foyer/Lobby next to northerly fire exit (Room 1/002)	Does not contain asbestos.
180.	As NG001602	Wall panel	Staircase/Stairwell (Room 1/003)	Does not contain asbestos.

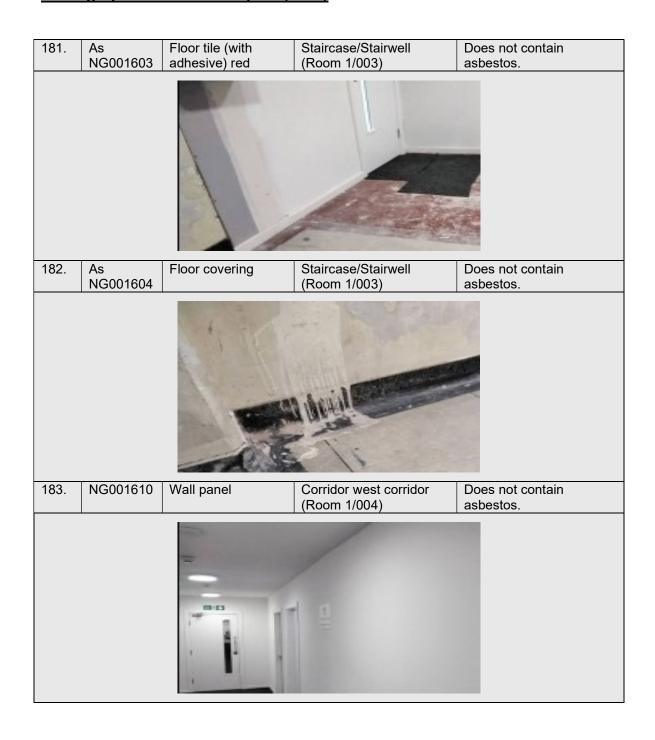

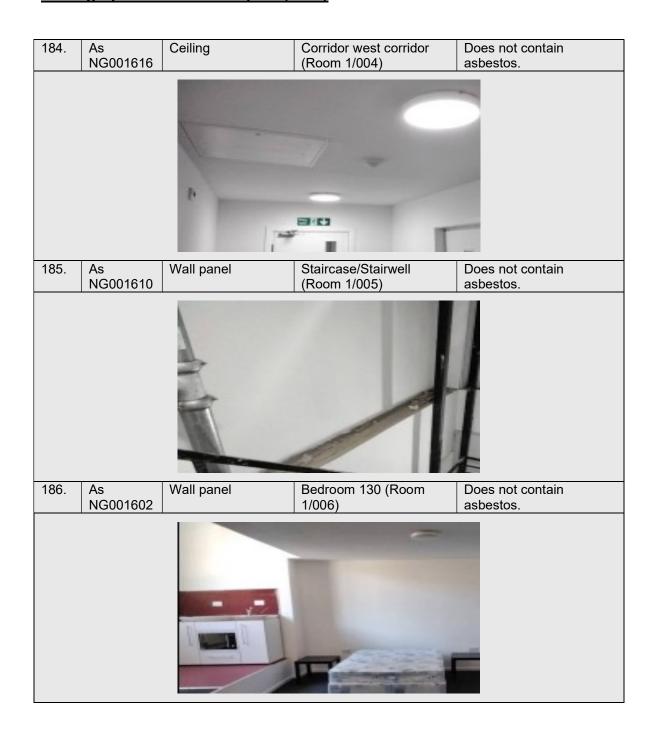

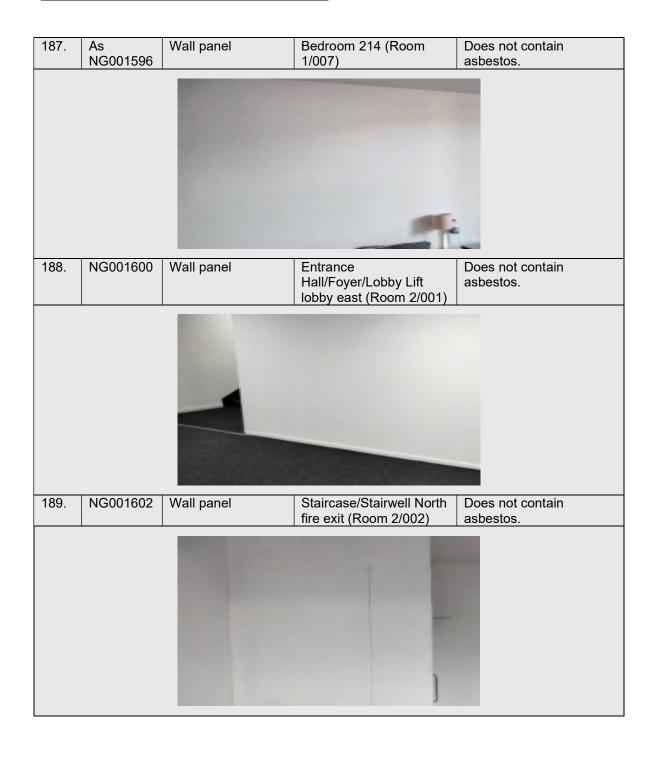

190.	NG001603	Floor tile with adhesive (red)	Staircase/Stairwell North fire exit (Room 2/002)	Does not contain asbestos.
191.	NG001604	Floor covering	Staircase/Stairwell North fire exit (Room 2/002)	Does not contain asbestos.
192.	As NG001602	Wall panel	Hallway/passageway Passage to Northerly fire exit (Room 2/003)	Does not contain asbestos.

193.	As NG001602	Wall panel	Bedroom 230 (Room 2/004)	Does not contain asbestos.
194.	NG001605	Wall panel	Corridor East Corridor (Room 2/005)	Does not contain asbestos.
195.	NG001613	Ceiling	Corridor East Corridor (Room 2/005)	Does not contain asbestos.


196.	NG001606	Wall panel	Staircase/Stairwell (Room 2/006)	Does not contain asbestos.
197.	As NG001606	Wall panel	Kitchen adjacent service cupboard (Room 2/007)	Does not contain asbestos.
400	NOOC 4 CO			
198.	NG001607	Wall panel	Entrance Hall/Foyer/Lobby to emergency exit (Room 2/008)	Does not contain asbestos.

199.	NG001608	Wall coating	Staircase/Stairwell Emergency fire exit (Room 2/009)	Does not contain asbestos.
			D-B	
200.	As NG001596	Wall panel	Bedroom 214 (Room 2/010)	Does not contain asbestos.
201.	As NG001613	Ceiling	Corridor West corridor (Room 2/011)	Does not contain asbestos.


202.	NG001594	Wall panel	Staircase/Stairwell fire exit staircase (Room 3/001)	Does not contain asbestos.
		3		
203.	NG001595	Floor tile with adhesive	Staircase/Stairwell fire exit staircase (Room 3/001)	Does not contain asbestos.
204.	NG001596	Wall panel	Corridor East Corridor (Room 3/002)	Does not contain asbestos.
			SECTION AND DESCRIPTION OF THE PERSON NAMED IN COLUMN TWO IS NOT THE PERSON NAMED IN COLUMN TWO IS NAMED I	




208.	NG001598	Wall panel	Entrance Hall/Foyer/Lobby (Room 3/005)	Does not contain asbestos.
209.	NG001599	Wall panel	Staircase/Stairwell (Room 3/006)	Does not contain asbestos.
210.	As NG001599	Wall panel	Plant Room (Room 3/007)	Does not contain asbestos.

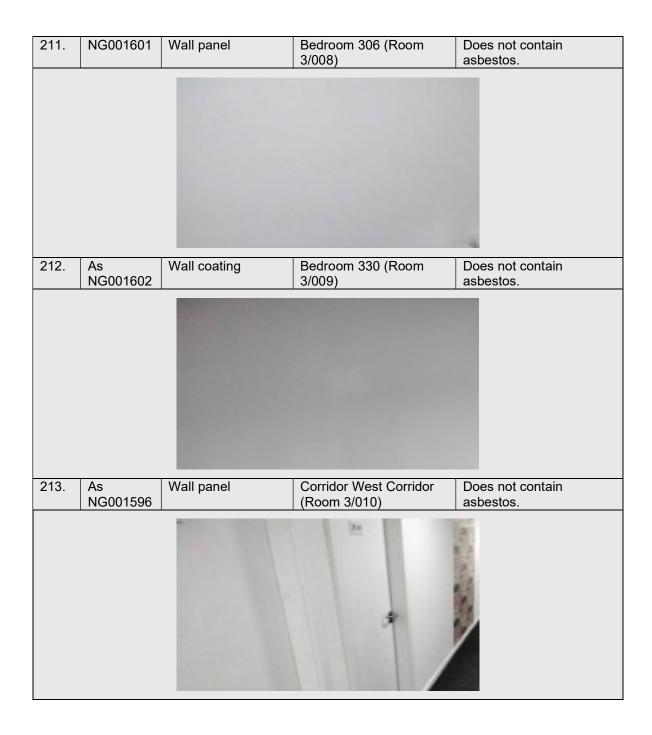


214.	As NG001614	Ceiling coating	Corridor West Corridor (Room 3/010)	Does not contain asbestos.
215.	NG001588	Wall coating to brickwork	Entrance Hall/Foyer/Lobby (Room 4/001)	Does not contain asbestos.
216.	NG001589	Wall panel	Entrance Hall/Foyer/Lobby (Room 4/001)	Does not contain asbestos.
			Please Constitution of the profession of the pro	

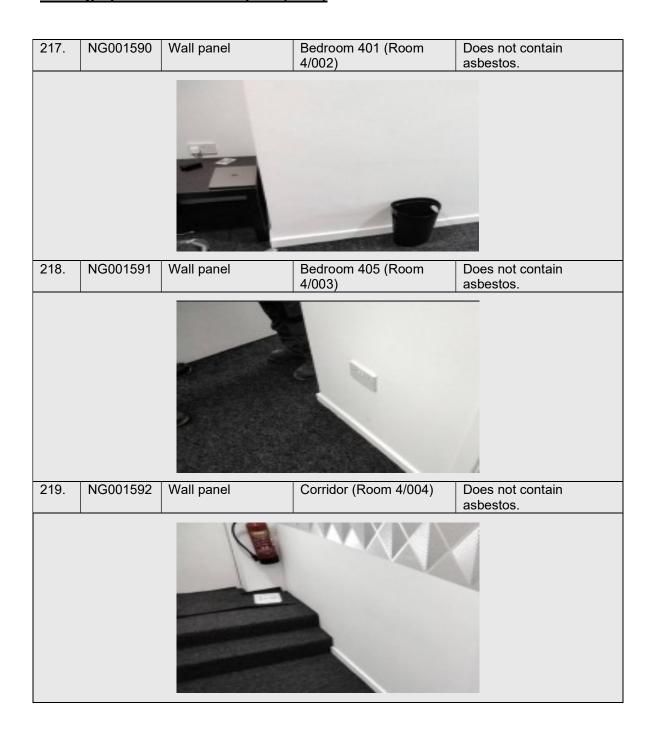

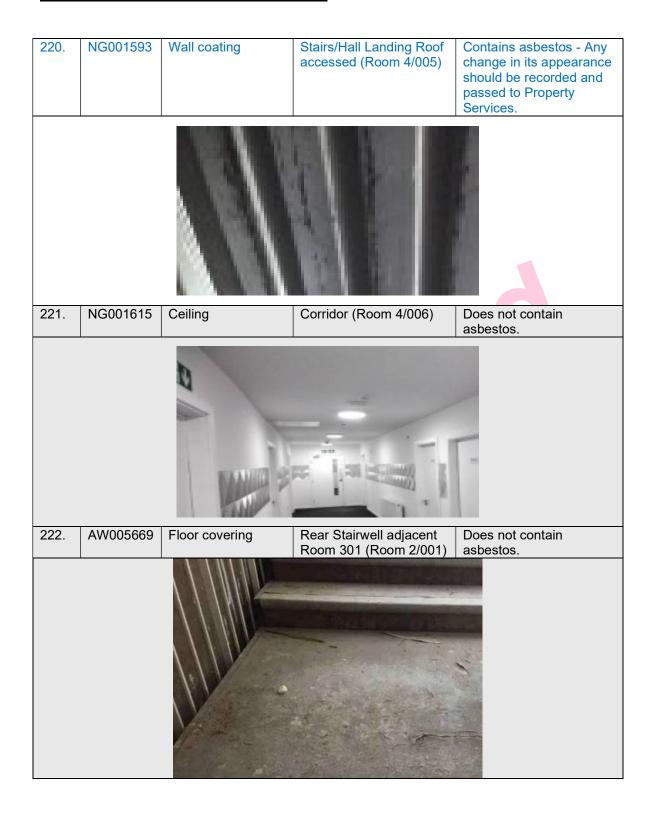





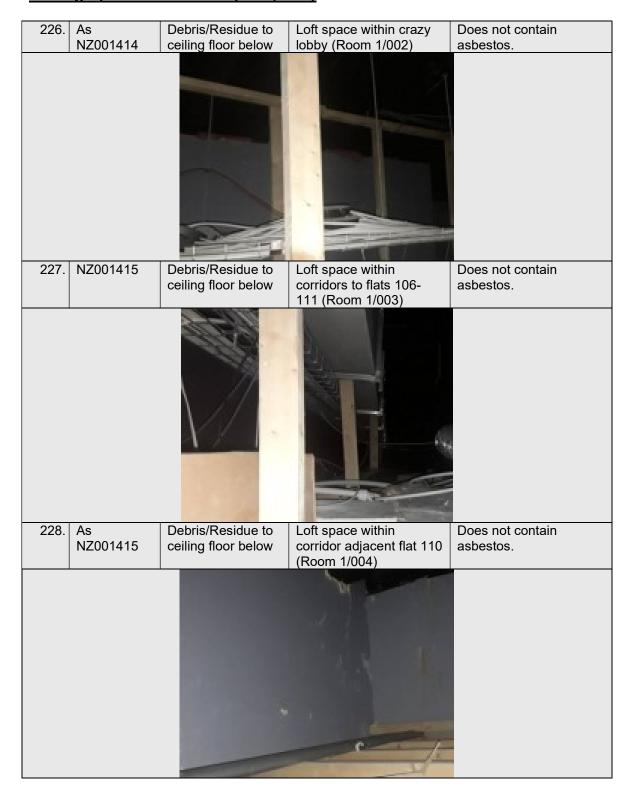


229.	NZ001416	Debris/Residue to ceiling floor below	Loft space within corridors to flats 112- 119 (Room 1/005)	Does not contain asbestos.
230.	As NZ001416	Debris/Residue to ceiling floor below	Loft space within corridors to flats 120- 125 (Room 1/006)	Does not contain asbestos.
231.	NZ001417	Debris/Residue to ceiling floor below	Loft space within corridors to flats 126- 130 (Room 1/007)	Does not contain asbestos.

232.	As NZ001417	Debris/Residue to ceiling floor below	Loft space within corridor adjacent flat 130 (Room 1/008)	Does not contain asbestos.
233.	NZ001418	Debris/Residue to ceiling floor below	Loft space within corridors to flats 101- 103 (Room 1/009)	Does not contain asbestos.
234.	As NZ001418	Debris/Residue to ceiling floor below	Loft space within corridors to flats 104- 105 (Room 1/010)	Does not contain asbestos.

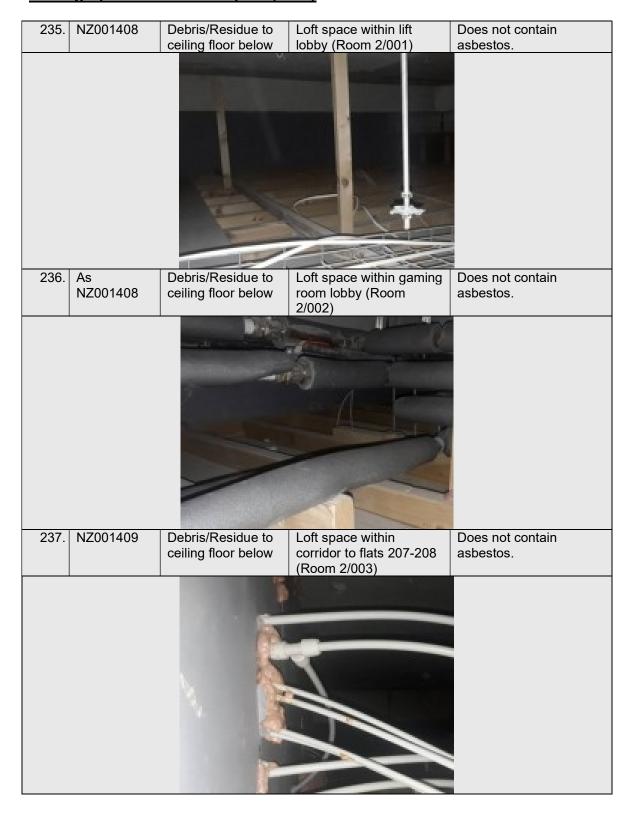

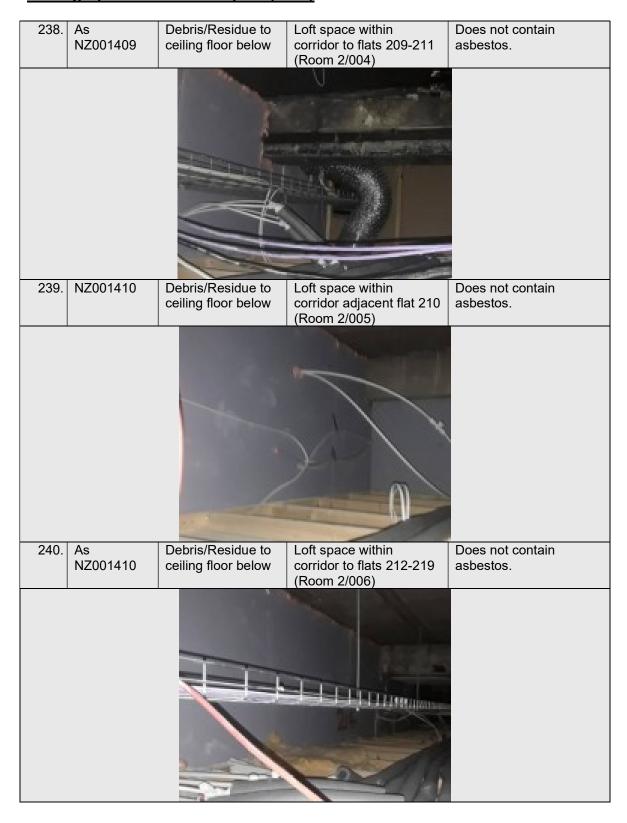

241.	NZ001411	Debris/Residue to ceiling floor below	Loft space within corridor to flats 220-225 (Room 2/007)	Does not contain asbestos.
242.	As NZ001411	Debris/Residue to ceiling floor below	Loft space within corridor adjacent lift lobby (Room 2/008)	Does not contain asbestos.
243.	NZ001412	Debris/Residue to ceiling floor below	Loft space within corridor to flats 226-230 (Room 2/009)	Does not contain asbestos.

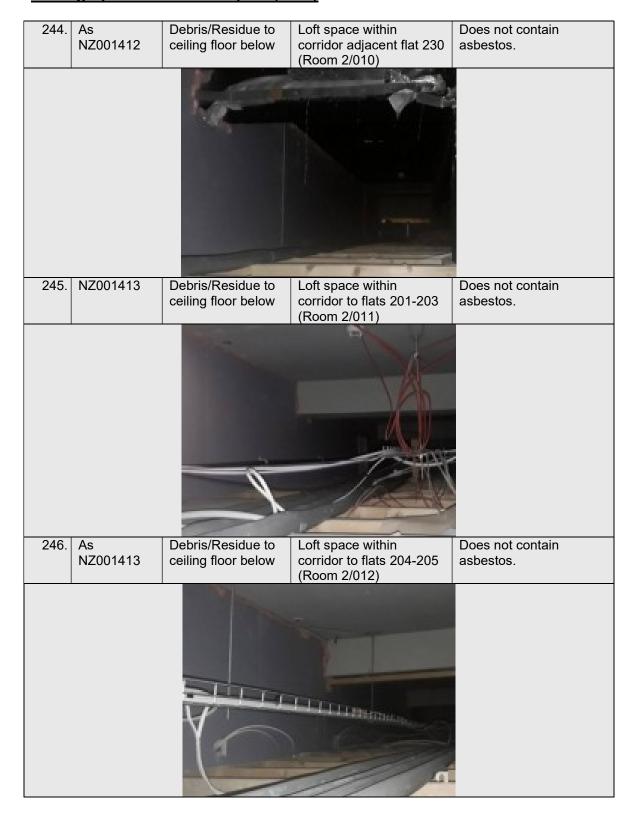



250.	As NZ001404	Debris/Residue to ceiling floor below	Loft space within corridor adjacent Flat 311 (Room 3/004)	Does not contain asbestos.
251.	NZ001405	Debris/Residue to ceiling floor below	Loft space within corridor to flats 312-319 (Room 3/005)	Does not contain asbestos.
252.	As NZ001405	Debris/Residue to ceiling floor below	Loft space within corridor to flats 320-325 (Room 3/006)	Does not contain asbestos.

253.	As NZ001404	Debris/Residue to ceiling floor below	Loft space within corridor adjacent Flat 321 (Room 3/007)	Does not contain asbestos.
254.	NZ001406	Debris/Residue to ceiling floor below	Loft space within corridor to flats 326-330 (Room 3/008)	Does not contain asbestos.
255.	As NZ001406	Debris/Residue to ceiling floor below	Loft space within corridor adjacent flat 330 (Room 3/009)	Does not contain asbestos.

256.	NZ001407	Debris/Residue to ceiling floor below	Loft space within corridor to flats 301-304 (Room 3/010)	Does not contain asbestos.
257.	As NZ001407	Debris/Residue to ceiling floor below	Loft space within corridor to flats 301-304 (Room 3/011)	Does not contain asbestos.
			Comment of the second	
258.	NZ001401	Debris/Residue to ceiling floor below	Loft space within corridor to flats 413-414 (Room 4/001)	Does not contain asbestos.

259.	As NZ001401	Debris/Residue to ceiling floor below	Loft space within corridor to flats 408-412 (Room 4/002)	Does not contain asbestos.
		II.		
260.	NZ001402	Debris/Residue to ceiling floor below	Loft space within corridor to flats 415-416 (Room 4/003)	Does not contain asbestos.
261.	As NZ001402	Debris/Residue to ceiling floor below	Loft space within corridor to flats 403-407 (Room 4/004)	Does not contain asbestos.

262.	EV005969	Textured coated wall & debris to ceiling loft space where the wall had been damaged to ducting installation	Loft space/Ceiling void (R/01)	Does not contain asbestos.



#### Five Simple Steps to Asbestos Management

Each property has a nominated site asbestos monitoring officer (SAMO). The SAMO is responsible for maintaining this register and ensuring all necessary personnel are aware of the register including all maintenance, construction and service installers; undertaking periodic inspections and liasing with the Departmental Asbestos Co-ordinator and the Asbestos Manager in Property Services as necessary.

The SAMO's role is very important but this guide is hoped to ensure the requirements are easy and simple to follow.

#### Step 1 – Receiving the Register

The SAMO is the tenant.

And the person is responsible for the register, where it is located and that it is kept up to date.

The register contains a plan of the premises and a photographic schedule of where the asbestos is and what risk is associated.

The SAMO must make all employees aware of the locations and should let any contractors entering the building view the register before any work is started.

#### Step 2 – Periodic Inspections

The SAMO must look at the locations photographed and compare the asbestos now to when the photograph was taken and complete the checklist attached (Form 2).

The checklists are to be completed periodically in accordance with the schedule attached.

Should the SAMO come across some asbestos which has been disturbed, whether during refurbishment works or during the normal course of wear and tear, they should complete Form 4 as far as possible and contact Property Services for advice and remedial action.

In the meantime, they should ensure that access to the area containing the disturbed or damaged asbestos is prohibited until Property Services has made recommendations.

#### Step 3 – Planned Work

All planned works that may disturb or danger any asbestos indicated, should be reported to Property Services using form 3 at <u>least 21 days</u> before the work is due to commence.

#### Step 4 – Contractors on Site

If a contractor arrives on site, the SAMO must:

- a. Make sure they read/view the register
- b. Get contractor to sign register to say he has read it (Form1).
- c. Get confirmation from the contractor that proposed works will not disturb any asbestos areas.
- d. If area is disturbed that was not identified in Register, advise Property Services immediately and complete Form 4.

#### Step 5 – Monitoring the Register

On completion of work get contractor to sign to say they didn't disturb any areas.

If alterations have occurred details should be forwarded to Property Services.

If you, as SAMO, are to leave your post, please notify your Departmental Coordinator to appoint another person and notify Property Services and the front of your register.

In the event of an exposure of asbestos, please refer to your site specific emergency procedures. However, as a minimum:

- Seal the area off completely. (Lock the area off if possible and post a notice on the door, "No access - Contact ..........")
- If there is any air movement systems within the premises, shut it off.
- Contact the Asbestos Manager on 07557 938966 immediately. Who will arrange for any remedial works / air monitoring.
- Start to complete the "Registration of Disturbances" form, which is in your register (Section 10 in the new style register).

Once the remedial works have been carried out and a clear air test certificate has been issued. Access to the area can be re-opened.

In the event that you are unable to contact the Asbestos Manager, please contact the Civic Centre on 520 5555 and ask for assistance from a building surveyor. Out of hours ring the City Alarm and Emergency Control room on 553 1999.

Central Safety can be contacted on 561 2311.

In the event of a fire (or drill), the asbestos register must be taken outside to show the emergency services.

#### Commonly Asked Questions.

#### How often should SAMO's undertake inspections of asbestos containing materials?

The Asbestos Manager will inform the SAMO of how often the inspections should be undertaken.

#### What should a SAMO do if the asbestos containing materials are disturbed or damaged?

The SAMO should prohibit access to the areas until the Asbestos Manager in Property Services has been contacted and given recommendations.

### Can employees put up decorations onto asbestos containing materials?

No decorations should be attached to asbestos containing materials. However, it is understood that some decoration is already attached to asbestos containing materials and these should be left in place.

#### Can a room with asbestos containing materials in the ceiling and wall be painted?

Yes, as long as the material is not rubbed or sanded down, as this may result in the release of asbestos fibres.

# Why isn't all asbestos containing materials removed from buildings? Because it is safer to leave asbestos containing materials in good condition in buildings. Removing the materials will result in a greater risk to health because of the consequential release of fibres.

## When will asbestos containing material be removed from my building?

Asbestos containing materials will be removed if work involves the disturbance of the material e.g. during the refurbishment or dismantling of part of the building or structure.

#### What should a SAMO do if he/she has had no training in use of the register?

The SAMO should ring the Departmental Co-ordinator who will arrange training.

INSPECTION SCHEDULE FORM 2

Item No.	Area Sampled	Location Name	Inspection Frequency	Date of Return	Condition Same/change	Action Required Y/N	Comments
1.	Floor tiles Grey/pink	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk				
2.	Debris/Residue to ceiling void and floor	Z-Sub level 1 Shop Floor (Room Z1/001)	This item is classed as low risk and should be inspected every 6 months	N/A	N/A	N/A	Removed Sept 2023
3.	Pipework Gaskets	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk				
4.	Pipework Gaskets to deeply recessed to sample	Z-Sub level 1 Shop Floor (Room Z1/001)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
5.	Cable braiding insulation	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk				
6.	Cable braiding insulation	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk				
7.	Fuses flashguards	Z-Sub level 1 Shop Floor (Room Z1/001)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
8.	Debris/Residue	Z-Sub level 1 Shop Floor (Room Z1/001)	This item is classed as very low risk and should be inspected every 12 months	N/A	N/A	N/A	Removed Sept 2023
9.	Debris/Residue from boiler room entrance across to stairs and adjacent areas	Z-Sub level 1 Shop Floor (Room Z1/001)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
10.	Debris/Residue to redundant pump	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk				

11.	Debris/Residue to floor adjacent stairwell	Z-Sub level 1 Shop Floor (Room Z1/001)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
12.	Ceiling tile behind metal grid tiles	Z-Sub level 1 Shop Floor (Room Z1/001)	No Risk				
13.	Ductwork joints	Z-Sub level 1 Shop Floor (Room Z1/001)	This item is classed as low risk and should be inspected every 6 months	05/01/24			
14.	Floor tile on shelving	Z-Sub level 1 Store Room (Room Z1/006)	No Risk				
15.	Debris/Residue to redundant pipe hanger	Z-Sub level 1 Switch Room (Room Z1/007)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
16.	Cable braiding insulation	Z-Sub level 1 Switch Room (Room Z1/007)	No Risk				
17.	Fuses flashguards	Z-Sub level 1 Switch Room (Room Z1/007)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
18.	Door seal/gasket discarded on floor	Z-Sub level 1 Switch Room (Room Z1/007)	No Risk				
19.	Debris/residue to floor	Z-Sub level 1 Plant Room (Room Z1/008)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
20.	Ductwork joints	Z-Sub level 1 Plant Room (Room Z1/008)	This item should be removed by a licensed contractor asap	N/A			
21.	Ductwork joints	Z-Sub level 1 Staircase/Stairwell (Room Z1/009)	This item is classed as low risk and should be inspected every 6 months	05/01/24			
22.	Wall	Z-Sub level 1	This item should be	N/A			

		Room (Room Z1/017)					
28.	Floor tile red		No Risk				
29.	Floor jointing compound	Z-Sub level 1 Tank Room (Room Z1/018)	No Risk				
30.	Floor tile cream	Z-Sub level 1 Tank Room (Room Z1/018)	No Risk				
31.	Fuses flashguards	Z-Sub level 1 Tank Room (Room Z1/018)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
32.	Pipework gaskets	Z-Sub level 1 Tank Room (Room Z1/018)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
33.	Pipework gaskets	Z-Sub level 1 Tank Room (Room Z1/018)	This item is classed as low risk and should be inspected every 6 months	05/01/24			
34.	Debris/Residue	Z-Sub level 1 Tank Room (Room Z1/018)	This item is classed as very low risk and	N/A	N/A	N/A	Removed Sept 2023

			should be inspected every 12 months				
35.	Floor tile pink grey	Z-Sub level 1 Shop Floor (Room Z1/019)	No Risk				
36.	Pipework Gaskets to deeply recessed to sample	Z-Sub level 1 Shop Floor (Room Z1/019)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
37.	Debris/Residue	Z-Sub level 1 Shop Floor (Room Z1/019)	This item is classed as very low risk and should be inspected every 12 months	N/A	N/A	N/A	Removed Sept 2023
38.	Ceiling tile behind metal grid tiles	Z-Sub level 1 Shop Floor (Room Z1/019)	No Risk				
39.	Floor tile cream	Z-Sub level 1 Shop Floor (Room Z1/019)	No Risk				
40.	Ductwork joints	Z-Sub level 1 Shop Floor (Room Z1/019)	This item is classed as low risk and should be inspected every 6 months	05/01/24	IN.		
41.	Floor tile pink/grey	Z-Sub level 1 Staircase/Stairwell (Room Z1/020)	No Risk				
42.	Debris/Reside to ceiling void and floor below	Z-Sub level 1 Store Room (Room Z1/021)	This item is classed as very low risk and should be inspected every 12 months	N/A	N/A	N/A	Removed Sept 2023
43.	Pipework Gaskets	Z-Sub level 1 Store Room (Room Z1/021)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
44.	Cable braiding/insulation	Z-Sub level 1 Store Room (Room Z1/022)	No Risk				
45.	Fuses flashguards	Z-Sub level 1 Store Room (Room Z1/023)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			

46.	Floor tile	Z-Sub level 1 Store Room (Room Z1/023)	No Risk				
47.	Floor tile grey	Z-Sub level 1 Store Room (Room Z1/026)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
48.	Floor tile grey	Z-Sub level 1 Store Room (Room Z1/027)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
49.	Debris/Residue broken boards	Z-Sub level 1 Store Room (Room Z1/027)	No Risk				
50.	Ductwork joints	Z-Sub level 1 Store Room (Room Z1/027)	This item is classed as low risk and should be inspected every 6 months	05/01/24			
51.	Fuses/flashguards inside fuses discarded throughout	Z-Sub level 1 Store Room (Room Z1/027)	No Risk				
52.	Debris/residue to floor	Z-Sub level 1 Store Room (Room Z1/027)	No Risk				
53.	Debris/residue to redundant hangers/equipment	Z-Sub level 1 Store Room (Room Z1/027)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
54.	Ductwork joints	Z-Sub level 1 Plant Room (Room Z1/028)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
55.	Ductwork joints	Z-Sub level 1 Store Room (Room Z1/029)	This item should be removed by a licensed contractor asap	N/A			
56.	Ductwork joints red/brown mastic	Z-Sub level 1 Store Room (Room Z1/029)	This item is classed as very low risk and should be inspected	05/07/24			

			every 12 months				
57.	Floor tile	Z-Sub level 1 Store Room (Room Z1/029)	No Risk				
58.	Debris/Residue to wall left of entrance	Z-Sub level 1 Boiler Room (Room Z1/030)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
59.	Debris/Residue to left wall	Z-Sub level 1 Boiler Room (Room Z1/030)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
60.	Ceiling Shuttering	Z-Sub level 1 Boiler Room (Room Z1/030)	This item is classed as very low risk and should be inspected every 12 months	05/07/24	V	21	
61.	Debris/Residue surrounding holes for flues	Z-Sub level 1 Boiler Room (Room Z1/030)	No Risk				
62.	Debris/Residue to rear RHS wall	Z-Sub level 1 Boiler Room (Room Z1/030)	This item is classed as a medium risk and should be inspected every 3 months	N/A	N/A	N/A	Removed Sept 2023
63.	Debris/Residue to floor	Z-Sub level 1 Boiler Room (Room Z1/030)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
64.	Debris/Residue to floor	Z-Sub level 1 Boiler Room (Room Z1/030)	No Risk				
65.	Floor tile	Z-Sub level 1 Boiler Room (Room Z1/030)	This item should be removed by a licensed contractor asap	N/A			
66.	Floor tile	Z-Sub level 1 Store Room (Room Z1/032)	No Risk				
67.	Pipework gasket	Z-Sub level 1 Store Room (Room Z1/032)	This item is classed as very low risk and should be inspected	05/07/24			

			every 12 months				
68.	Pipework wrap to pipe penetrations in ceiling	Z-Sub level 1 Store Room (Room Z1/032)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
69.	Floor tile pink/grey including debris up the stairs	Z-Sub level 1 Stairwell Staircase (Room Z1/034)	No Risk				
70.	Floor tile red	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
71.	Floor tile grey	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
72.	Floor adhesive remnants	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months	05/07/24	5		
73.	Window putty/seal adjacent main entrance damaged and in-situ	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
74.	Debris/Residue to entrance porch, on top and to sides, including beneath shelf and framework	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
75.	Debris/Residue to top of ceiling at entrance porch	Ground Floor Shop Floor Unit 1 (Room G/001)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
76.	Ceiling tile including debris to floor	Ground Floor Shop Floor Unit 1 (Room G/001)	No Risk				
77.	Wall coating, rear	Ground Floor Shop	No Risk				

	wall beneath skim	Floor Unit 1 (Room G/001)					
78.	Floor tile brown surrounding columns	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
79.	Debris/Residue surrounding feet of columns	Ground Floor Shop Floor Unit 1 (Room G/001)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
80.	Debris/Residue surrounding feet of columns	Ground Floor Shop Floor Unit 1 (Room G/001)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
81.	Floor nosing to stairs step up to window	Ground Floor Shop Floor Unit 1 (Room G/001)	This item is classed as very low risk and should be inspected every 12 months	05/07/24	100		
82.	Debris/Residue to floor	Ground Floor Porch Unit 1 (Room G/002)	This item is classed as very low risk and should be inspected every 12 months	N/A	N/A	N/A	Removed Sept 2023
83.	Ductwork joints	Ground Floor Porch Unit 1 (Room G/002)	This item is classed as low risk and should be inspected every 6 months	05/01/24			
84.	Floor adhesive remnants	Ground Floor Store Room Unit 1 (Room G/003)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
85.	Floor adhesive remnants	Ground Floor Store Room Unit 1 (Room G/004)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
86.	Floor tile grey/beige beneath modern lino	Ground Floor Store Room Bike Store (Room G/005)	This item is classed as very low risk and should be inspected	05/07/24			

			every 12 months				
87.	Ceiling shuttering	Ground Floor Store Room Bike Store (Room G/005)	No Risk				
88.	Tile grey/beige beneath carpet	Ground Floor Laboratory (Room G/007)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
89.	Tile grey/beige beneath modern lino	Ground Floor Hallway/passageway Switch Room (Room G/008)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
90.	Pipework Gasket	Ground Floor Hallway/passageway Switch Room (Room G/008)	No Risk				
91.	Cable braiding insulation	Ground Floor Switch Room behind lifts (Room G/009)	No Risk				
92.	Floor jointing compound	Ground Floor Switch Room behind lifts (Room G/009)	No Risk				
93.	Floor adhesive remnants beneath carpet	Ground Floor Hallway/passageway lift lobby (Room G/010)	No Risk				
94.	Debri/Residue to wall, mid landing	Ground Floor Staircase/Stairwell (Room G/012)	No Risk				
95.	Debris/Residue	Ground Floor Staircase/Stairwell (Room G/014)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
96.	Floor tile grey/beige within electrical boxing to wall cavity and floor	Ground Floor Staircase/Stairwell (Room G/014)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
97.	Floor jointing	Ground Floor	No Risk				

	compound	Staircase/Stairwell (Room G/014)					
98.	Floor tile grey/beige carpet	Ground Floor Office (Room G/015)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
99.	Floor jointing compound	Ground Floor Store Room (Room G/017)	No Risk				
100.	Pipework insulation in wall penetration	Ground Floor Store Room (Room G/017)	This item is classed as low risk and should be inspected every 6 months	05/01/24			
101.	Floor adhesive remnants	Ground Floor Store Room (Room G/017)	No Risk				
102.	Floor tile grey/beige carpet	Ground Floor Store Room (Room G/017)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
103.	Wall to nail/screw heads, various points on column	Ground Floor Store Room (Room G/017)	No Risk				
104.	Floor jointing compound	Ground Floor Store Room unit 4 (Room G/018)	No Risk				
105.	Floor adhesive remnants	Ground Floor Store Room unit 4 (Room G/018)	No Risk				
106.	Pipework insulation packing to former wall penetration	Ground Floor Store Room unit 4 (Room G/018)	This item should be removed by a licensed contractor asap	N/A			
107.	Residue/Debris to floor	Ground Floor Store Room unit 4 (Room G/018)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
108.	Floor jointing compound	Ground Floor Store Room (Room G/020)	No Risk				

109.	Floor adhesive remnants	Ground Floor Store Room (Room G/020)	No Risk				
110.	Cabling braiding insulation	Ground Floor Store Room (Room G/020)	No Risk				
111.	Pipework gasket too deeply recessed to sample	Ground Floor Unit 3 (café) limited inspection to ceiling (Room G/022)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
112.	Wall to nail/screw heads various points on column	Ground Floor Unit 3 (café) limited inspection to ceiling (Room G/022)	No Risk				
113.	Floor adhesive remnants	Ground Floor Unit 3 (café) limited inspection to ceiling (Room G/022)	No Risk				
114.	Floor tile remnants	Ground Floor Unit 3 (café) limited inspection to ceiling (Room G/022)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
115.	Floor adhesive remnants	Ground Floor Shop Floor former store entrance (Room G/023)	No Risk				
116.	Floor tile remnants	Ground Floor Shop Floor former store entrance (Room G/023)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
117.	Debris/Residue to both floor voids adjacent front doors also on roller shutter	Ground Floor Shop Floor former store entrance (Room G/023)	This item is classed as very low risk and should be inspected every 12 months	N/A	N/A	N/A	Removed Sept 2023
118.	Floor adhesive remnants	Ground Floor Office (Room G/026)	No Risk				
119.	Floor adhesive remnants	Ground Floor Hallway/passageway (Room G/027)	No Risk				
120.	Floor adhesive remnants	Ground Floor Hallway/passageway (Room G/028)	No Risk				

121.	Ceiling tiles	Ground Floor Bin store (Room G/031)	No Risk			
122.	Floor adhesive remnants	Ground Floor Bin store (Room G/031)	No Risk			
123.	Ceiling tiles	Ground Floor Store Room (Room G/032)	No Risk			
124.	Floor adhesive remnants	Ground Floor Store Room (Room G/032)	No Risk			
125.	Floor adhesive remnants	Ground Floor Staff Room (Room G/035)	No Risk			
126.	Floor adhesive remnants	Ground Floor Office (Room G/036)	No Risk			
127.	Floor adhesive remnants	Ground Floor Entrance Hall/Foyer/Lobby (Room G/037)	No Risk			
128.	Floor adhesive remnants	Ground Floor Hallway/Passageway (Room G/038)	No Risk			
129.	Floor tile to former shop floor and understairs area	Ground Floor Staircase/Stairwell (Room G/039)	This item is classed as very low risk and should be inspected every 12 months	05/07/24		
130.	Floor adhesive remnants	Ground Floor Staircase/Stairwell (Room G/039)	No Risk			
131.	Wall – within hole in wall under stairs	Ground Floor Staircase/Stairwell (Room G/039)	No Risk			
132.	Window putty/seal to discarded window	Ground Floor Staircase/Stairwell (Room G/039)	This item is classed as very low risk and should be inspected every 12 months	05/07/24		
133.	Floor tile	First Floor Plant Room (Room 1/005)	No Risk			
134.	Floor tile beneath carpet	Second Floor Landing including stairs up	No Risk			

		(Room 2/001)					
135.	Floor tile beneath	Second Floor Landing	No Risk				
	carpet	(Room 2/003)					
136.	Floor tile	Second Floor Plant	No Risk				
		Room (Room 2/004)					
137.	Wall Coating	Second Floor Plant	No Risk				
		Room (Room 2/004)					
138.	Wall void cavity	Second Floor Plant	No Risk				
		Room (Room 2/004)					
139.	Ceiling void	Second Floor	No Risk				
	insulation top	Hallway/passageway					
	Of ceiling heater	(Room 2/010)					
140.	Floor tile beneath	Second Floor	No Risk				
	carpet	Hallway/passageway					
		(Room 2/013)					
141.	Debris/Residue to	Second Floor Fire	This item should be	N/A	N/A	N/A	Removed Sept 2023
	stairs	escape (Room 2/015)	removed by a				
			licensed contractor				
			asap				
142.	Debris/Residue to	Second Floor Fire	This item should be	N/A	N/A	N/A	Removed Sept 2023
	side stairs (external	escape (Room 2/015)	removed by a				
	wall) including		licensed contractor				
440	sloping runner	O. J.Fl. Fin	asap	05/07/04			
143.	Floor nosing to	Second Floor Fire	This item is classed	05/07/24			
	stairs	escape (Room 2/015)	as very low risk and				
			should be inspected				
444	[] +!  -   + -	Second Floor	every 12 months				
144.	Floor tile beneath		No Risk				
	carpet	Hallway/passageway					
145.	Floor tile beneath	(Room 2/016) Second Floor	No Risk				
145.		Hallway/passageway	INU IXISK				
	carpet	(Room 2/017)					
146.	Floor tile beneath	Second Floor Store	No Risk				
140.	carpet	Room (Room 2/018)	INO INISK				
147.	Pipework lining to	Second Floor Store	This item should be	N/A	N/A	N/A	Pomovod Sont 2022
147.	Fipework lifting to	Second Floor Store	THIS ILETTI SHOULD DE	IW/A	IV/A	IN/A	Removed Sept 2023

	insulation remnants	Room (Room 2/018)	removed by a licensed contractor asap				
148.	Window/putty seal from removed window	Second Floor Store Room (Room 2/018)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
149.	Floor tile beneath carpet	Second Floor Store Room Former toilets (Room 2/019)	No Risk				
150.	Ductwork	Second Floor Store Room Former toilets (Room 2/019)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
151.	Ceiling void ceiling above panel	Third Floor Landing (Room 3/001)	This item is classed as low risk and should be inspected every 6 months	05/01/24			
152.	Wall tile	Third Floor Plant Room (Room 3/004)	No Risk				
153.	Debris/Residue to stairs	Third Floor Fire Escape (Room 3/016)	This item is classed as low risk and should be inspected every 6 months	05/01/24			
154.	Ceiling sloping Packing to girders	Third Floor Fire Escape (Room 3/016)	No Risk				
155.	Pipework lining to insulation remnants to 2 large pipes and floor	Third Floor Store Room (Room 3/021)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
156.	Pipework gaskets	Third Floor Store Room (Room 3/021)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
157.	Pipework gaskets too deeply recessed to sample	Third Floor Store Room (Room 3/023)	This item is classed as very low risk and should be inspected	05/07/24			

			every 12 months				
158.	Beam cladding suspected continuation from electric cupboard	Fourth Floor Landing (Room 4/001)	This item is classed as very low risk and should be inspected every 12 months	05/07/24			
159.	Beam cladding beneath skim, sampled via pre- existing damage to skim	Fourth Floor Electric cupboard (Room 4/002)	This item should be removed by a licensed contractor asap	N/A			
160.	Beam cladding remnants beneath girder	Fourth Floor Hub/Network Room (Room 4/006)	This item is classed as very low risk and should be inspected every 12 months	05/07/24	70		
161.	Debris/Reside to steel girder	Fourth Floor Hub/Network Room (Room 4/006)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
162.	Debris/Residue	Fourth Floor Hub/Network Room (Room 4/006)	No Risk				
163.	Beam cladding remnants beneath girder	Fourth Floor Plant Room (Room 4/007)	This item should be removed by a licensed contractor asap	N/A	N/A	N/A	Removed Sept 2023
164.	Debris/Reside to steel girder	Fourth Floor Plant Room (Room 4/007)	This item is classed as low risk and should be inspected every 6 months	N/A	N/A	N/A	Removed Sept 2023
165.	Debris/Residue	Fourth Floor Plant Room (Room 4/007)	No Risk				
166.	Tank pacing to brackets	Fourth Floor Plant Room (Room 4/007)	No Risk				
167.	Damp proof course surrounding windows	Fourth Floor Plant Room (Room 4/007)	No Risk				
168.	Fuses/flashguards	Fourth Floor Lift	This item is classed	05/07/24			

169.	Fuses/flashguards isolation strips	Machinery Room (Room 4/008)  Fourth Floor Lift Machinery Room (Room 4/008)	as very low risk and should be inspected every 12 months This item is classed as very low risk and should be inspected every 12 months	05/07/24			
170.	Roof felt remnants to concrete	Fourth Floor Fire escape (Room 4/058)	No Risk				
171.	Wall coating to upper metal cladding	Fourth Floor External roof area (Room 4/059)	This item is classed as very low risk and should be inspected every 12 months	05/07/24	Vic	91	
172.	Pipework gaskets to sprinkler system	Mezzanine Switch Room midway between basement and ground floor	This item is classed as very low risk and should be inspected every 12 months	05/07/24	me		
173.	Wall panel	Ground Floor, Laundry (Room G/001)	No Risk				
174.	Floor tile (with adhesive) grey beneath carpet	Ground Floor, Laundry (Room G/001)	This item is classed as low risk and should be inspected every 6 months	05/01/24			
175.	Wall panel	Ground Floor, Entrance Hall/Foyer/Lobby Main lift lobby (Room G/002)	No Risk				
176.	Ceiling	Ground Floor, Entrance Hall/Foyer/Lobby Main lift lobby (Room G/002)	No Risk				
177.	Wall panel	First Floor, Entrance Hall/Foyer/Lobby Main lift lobby (Room 1/001)	No Risk				
178.	Ceiling	First Floor, Entrance Hall/Foyer/Lobby Main lift lobby (Room 1/001)	No Risk				

179.	Wall panel	First Floor, Entrance Hall/Foyer/Lobby next to northerly fire exit (Room 1/002)	No Risk		
180.	Wall panel	Staircase/Stairwell (Room 1/003)	No Risk		
181.	Floor tile (with adhesive) red	Staircase/Stairwell (Room 1/003)	No Risk		
182.	Floor covering	Staircase/Stairwell (Room 1/003)	No Risk		
183.	Wall panel	Corridor west corridor (Room 1/004)	No Risk		
184.	Ceiling	Corridor west corridor (Room 1/004)	No Risk		
185.	Wall panel	Staircase/Stairwell (Room 1/005)	No Risk		
186.	Wall panel	Bedroom 130 (Room 1/006)	No Risk		
187.	Wall panel	Bedroom 214 (Room 1/007)	No Risk		
188.	Wall panel	Entrance Hall/Foyer/Lobby Lift lobby east (Room 2/001)	No Risk		
189.	Wall panel	Staircase/Stairwell North fire exit (Room 2/002)	No Risk		
190.	Floor tile with adhesive (red)	Staircase/Stairwell North fire exit (Room 2/002)	No Risk		
191.	Floor covering	Staircase/Stairwell North fire exit (Room 2/002)	No Risk		
192.	Wall panel	Hallway/passageway Passage to Northerly fire exit (Room 2/003)	No Risk		
193.	Wall panel	Bedroom 230 (Room 2/004)	No Risk		
194.	Wall panel	Corridor East Corridor (Room 2/005)	No Risk		

195.	Ceiling	Corridor East Corridor			
		(Room 2/005)	No Risk		
196.	Wall panel	Staircase/Stairwell			
		(Room 2/006)	No Risk		
197.	Wall panel	Kitchen adjacent service			
		cupboard (Room 2/007)	No Risk		
198.	Wall panel	Entrance			
		Hall/Foyer/Lobby Lobby			
		to emergency exit			
		(Room 2/008)	No Risk		
199.	Wall coating	Staircase/Stairwell			
		Emergency fire exit			
		(Room 2/009)	No Risk		
200.	Wall panel	Bedroom 214 (Room			
		2/010)	No Risk		
201.	Ceiling	Corridor West corridor			
		(Room 2/011)	No Risk		
202.	Wall panel	Staircase/Stairwell fire			
		exit staircase (Room			
		3/001)	No Risk		
203.	Floor tile with	Staircase/Stairwell fire			
	adhesive	exit staircase (Room			
		3/001)	No Risk		
204.	Wall panel	Corridor East Corridor			
	·	(Room 3/002)	No Risk		
205.	Ceiling coating	Corridor East Corridor			
		(Room 3/002)	No Risk		
206.	Floor tile with	Hallway/Passageway			
	adhesive	(Room 3/003)	No Risk		
207.	Wall panel	Staircase/Stairwell			
	•	South stairwell (Room			
		3/004)	No Risk		
208.	Wall panel	Entrance			
		Hall/Foyer/Lobby (Room			
		3/005)	No Risk		
209.	Wall panel	Staircase/Stairwell	No Risk		

		(Room 3/006)				
210.	Wall panel	Plant Room (Room				
		3/007)	No Risk			
211.	Wall panel	Bedroom 306 (Room				
		3/008)	No Risk			
212.	Wall coating	Bedroom 330 (Room				
		3/009)	No Risk			
213.	Wall panel	Corridor West Corridor				
		(Room 3/010)	No Risk			
214.	Ceiling coating	Corridor West Corridor				
		(Room 3/010)	No Risk			
215.	Wall coating to	Entrance				
	brickwork	Hall/Foyer/Lobby (Room	N. D. I			
040	\A/- II I	4/001)	No Risk			
216.	Wall panel	Entrance				
		Hall/Foyer/Lobby (Room 4/001)	No Risk			
217.	Wall panel	Bedroom 401 (Room	INO KISK			
217.	vvali pariei	4/002)	No Risk			
218.	Wall panel	Bedroom 405 (Room	TVO TVISIV			
210.	vvan parior	4/003)	No Risk			
219.	Wall panel	Corridor (Room 4/004)	No Risk			
220.	Wall coating	Stairs/Hall Landing Roof	This item is classed	05/01/24		
		accessed (Room 4/005)	as low risk and	00/01/21		
			should be inspected			
			every 6 months			
221.	Ceiling	Corridor (Room 4/006)	No Risk			
222.	Floor covering	Rear stairwell adjacent				
		Rm 301 (Room 2/001)	No Risk			
223.	Ceiling void –	Corridor adjacent Rm				
	residue to	214 (Room 2/002)				
	redundant radiator		No Risk			
224.	Ceiling void – paint	Corridor adjacent Rm				
	coating to ceiling	316 (Room 3/001)	No Risk			
225.	Debris/Residue to	Loft space within lift	N. 5			
	ceiling floor below	lobby (Room 1/001)	No Risk			

226.	Debris/Residue to	Loft space within crazy			
	ceiling floor below	lobby (Room 1/002)	No Risk		
227.	Debris/Residue to	Loft space within			
	ceiling floor below	corridors to flats 106-			
		111 (Room 1/003)	No Risk		
228.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor adjacent flat 110			
		(Room 1/004)	No Risk		
229.	Debris/Residue to	Loft space within			
	ceiling floor below	corridors to flats 112-			
		119 (Room 1/005)	No Risk		
230.	Debris/Residue to	Loft space within			
	ceiling floor below	corridors to flats 120-			
		125 (Room 1/006)	No Risk		
231.	Debris/Residue to	Loft space within			
	ceiling floor below	corridors to flats 126-			
		130 (Room 1/007)	No Risk		
232.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor adjacent flat 130			
		(Room 1/008)	No Risk		
233.	Debris/Residue to	Loft space within			
	ceiling floor below	corridors to flats 101-			
		103 (Room 1/009)	No Risk		
234.	Debris/Residue to	Loft space within			
	ceiling floor below	corridors to flats 104-			
		105 (Room 1/010)	No Risk		
235.	Debris/Residue to	Loft space within lift			
	ceiling floor below	lobby (Room 2/001)	No Risk		
236.	Debris/Residue to	Loft space within gaming			
	ceiling floor below	room lobby (Room			
		2/002)	No Risk		
237.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor to flats 207-208			
		(Room 2/003)	No Risk		
238.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor to flats 209-211	No Risk		

		(Room 2/004)			
239.	Debris/Residue to ceiling floor below	Loft space within corridor adjacent flat 210 (Room 2/005)	No Risk		
240.	Debris/Residue to ceiling floor below	Loft space within corridor to flats 212-219 (Room 2/006)	No Risk		
241.	Debris/Residue to ceiling floor below	Loft space within corridor to flats 220-225 (Room 2/007)	No Risk		
242.	Debris/Residue to ceiling floor below	Loft space within corridor adjacent lift lobby (Room 2/008)	No Risk		
243.	Debris/Residue to ceiling floor below	Loft space within corridor to flats 226-230 (Room 2/009)	No Risk		
244.	Debris/Residue to ceiling floor below	Loft space within corridor adjacent flat 230 (Room 2/010)	No Risk		
245.	Debris/Residue to ceiling floor below	Loft space within corridor to flats 201-203 (Room 2/011)	No Risk		
246.	Debris/Residue to ceiling floor below	Loft space within corridor to flats 204-205 (Room 2/012)	No Risk		
247.	Debris/Residue to ceiling floor below	Loft space within lobby (Room 3/001)	No Risk		
248.	Debris/Residue to ceiling floor below	Loft space within football pool room lobby (Room 3/002)	No Risk		
249.	Debris/Residue to ceiling floor below	Loft space within corridor to flats 306-311 (Room 3/003)	No Risk		
250.	Debris/Residue to ceiling floor below	Loft space within corridor adjacent Flat 311 (Room 3/004)	No Risk		

251.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor to flats 312-319			
	3	(Room 3/005)	No Risk		
252.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor to flats 320-325			
		(Room 3/006)	No Risk		
253.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor adjacent Flat			
		321 (Room 3/007)	No Risk		
254.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor to flats 326-330			
		(Room 3/008)	No Risk		
255.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor adjacent flat 330			
		(Room 3/009)	No Risk		
256.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor to flats 301-304			
0==	D 1 1 /D 11 /	(Room 3/010)	No Risk		
257.	Debris/Residue to	Loft space within			
	ceiling floor below	corridor to flats 301-304	Na Diale		
250	Debris/Residue to	(Room 3/011)	No Risk		
258.		Loft space within corridor to flats 413-414			
	ceiling floor below		No Diek		
259.	Debris/Residue to	(Room 4/001)  Loft space within	No Risk		
259.		corridor to flats 408-412			
	ceiling floor below	(Room 4/002)	No Risk		
260.	Debris/Residue to	Loft space within	INO IXISK		
200.	ceiling floor below	corridor to flats 415-416			
	Coming noor below	(Room 4/003)	No Risk		
261.	Debris/Residue to	Loft space within	110 11011		
201.	ceiling floor below	corridor to flats 403-407			
		(Room 4/004)	No Risk		
262.	Textured coated	Loft space/Ceiling void			
	wall & debris to	(R/01)			
	ceiling loft space	, ,			
	where the wall had		No Risk		

been damaged to			
ducting installation			



#### **Good Practice Guidance:**

- Take photographs of ACMs for each inspection and store for future reference
- Compare previous photographs with current condition state to determine whether there has been any deterioration the last inspection
- Replace missing/damaged asbestos labels/stickers

#### **Comments:**



School/Site:	
Date of inspection:	
Inspected by (signature):	
Print Name:	
